Programme

Greyline
Taking care of homes

ID	Task Mode	Task Name	Duration	Start	Finish
1		**Non-Scaffold Dependant**	**44 days**	**Mon 24/11/25**	**Wed 11/02/26**
2		R&D Survey- 30/ week	16 days	Mon 24/11/25	Mon 15/12/25
3		Loft Insulation	32 days	Wed 10/12/25	Wed 11/02/26
4		Ventilation	28 days	Mon 08/12/25	Tue 03/02/26
5		Door Undercuts	18 days	Mon 01/12/25	Tue 13/01/26
6					
7		**Week 1 - 15 properties**	**11 days**	**Mon 12/01/26**	**Mon 26/01/26**
8		Scaffold- 3 gangs	5 days	Mon 12/01/26	Fri 16/01/26
9		Windows and Doors- 4 gangs	6 days	Wed 14/01/26	Wed 21/01/26
10		CWI EXTRACT AND REPLACE- 1 GANG, 3 PROPS PER DAY	5 days	Fri 16/01/26	Thu 22/01/26
11		Scaffold Strike	5 days	Tue 20/01/26	Mon 26/01/26
12		**Week 2 - 15 properties**	**11 days**	**Mon 19/01/26**	**Mon 02/02/26**
13		Scaffold- 3 gangs	5 days	Mon 19/01/26	Fri 23/01/26
14		Windows and Doors- 4 gangs	6 days	Wed 21/01/26	Wed 28/01/26
15		CWI EXTRACT AND REPLACE- 1 GANG, 3 PROPS PER DAY	5 days	Fri 23/01/26	Thu 29/01/26
16		Scaffold Strike	5 days	Tue 27/01/26	Mon 02/02/26
17		**Week 3 - 15 properties**	**11 days**	**Mon 26/01/26**	**Mon 09/02/26**
18		Scaffold- 3 gangs	5 days	Mon 26/01/26	Fri 30/01/26
19		Windows and Doors- 4 gangs	6 days	Wed 28/01/26	Wed 04/02/26
20		CWI EXTRACT AND REPLACE- 1 GANG, 3 PROPS PER DAY	5 days	Fri 30/01/26	Thu 05/02/26
21		Scaffold Strike	5 days	Tue 03/02/26	Mon 09/02/26
22		**Week 4 - 15 properties**	**11 days**	**Mon 02/02/26**	**Mon 16/02/26**
23		Scaffold- 3 gangs	5 days	Mon 02/02/26	Fri 06/02/26
24		Windows and Doors- 4 gangs	6 days	Wed 04/02/26	Wed 11/02/26
25		CWI EXTRACT AND REPLACE- 1 GANG, 3 PROPS PER DAY	5 days	Fri 06/02/26	Thu 12/02/26
26		Scaffold Strike	5 days	Tue 10/02/26	Mon 16/02/26
27		**Week 5 - 15 properties**	**16 days**	**Mon 09/02/26**	**Mon 02/03/26**
28		Scaffold- 3 gangs	5 days	Mon 09/02/26	Fri 13/02/26
29		Windows and Doors- 4 gangs	6 days	Wed 11/02/26	Wed 18/02/26
30		CWI EXTRACT AND REPLACE- 1 GANG, 3 PROPS PER DAY	5 days	Fri 13/02/26	Thu 19/02/26
31		Scaffold Strike	5 days	Tue 17/02/26	Mon 23/02/26
32		**Week 6 - 10 properties, plus mop-up**	**11 days**	**Mon 16/02/26**	**Mon 02/03/26**
33		Scaffold- 3 gangs	5 days	Mon 16/02/26	Fri 20/02/26
34		Windows and Doors- 4 gangs	6 days	Wed 18/02/26	Wed 25/02/26
35		CWI EXTRACT AND REPLACE- 1 GANG, 3 PROPS PER DAY	5 days	Fri 20/02/26	Thu 26/02/26
36		Scaffold Strike	5 days	Tue 24/02/26	Mon 02/03/26

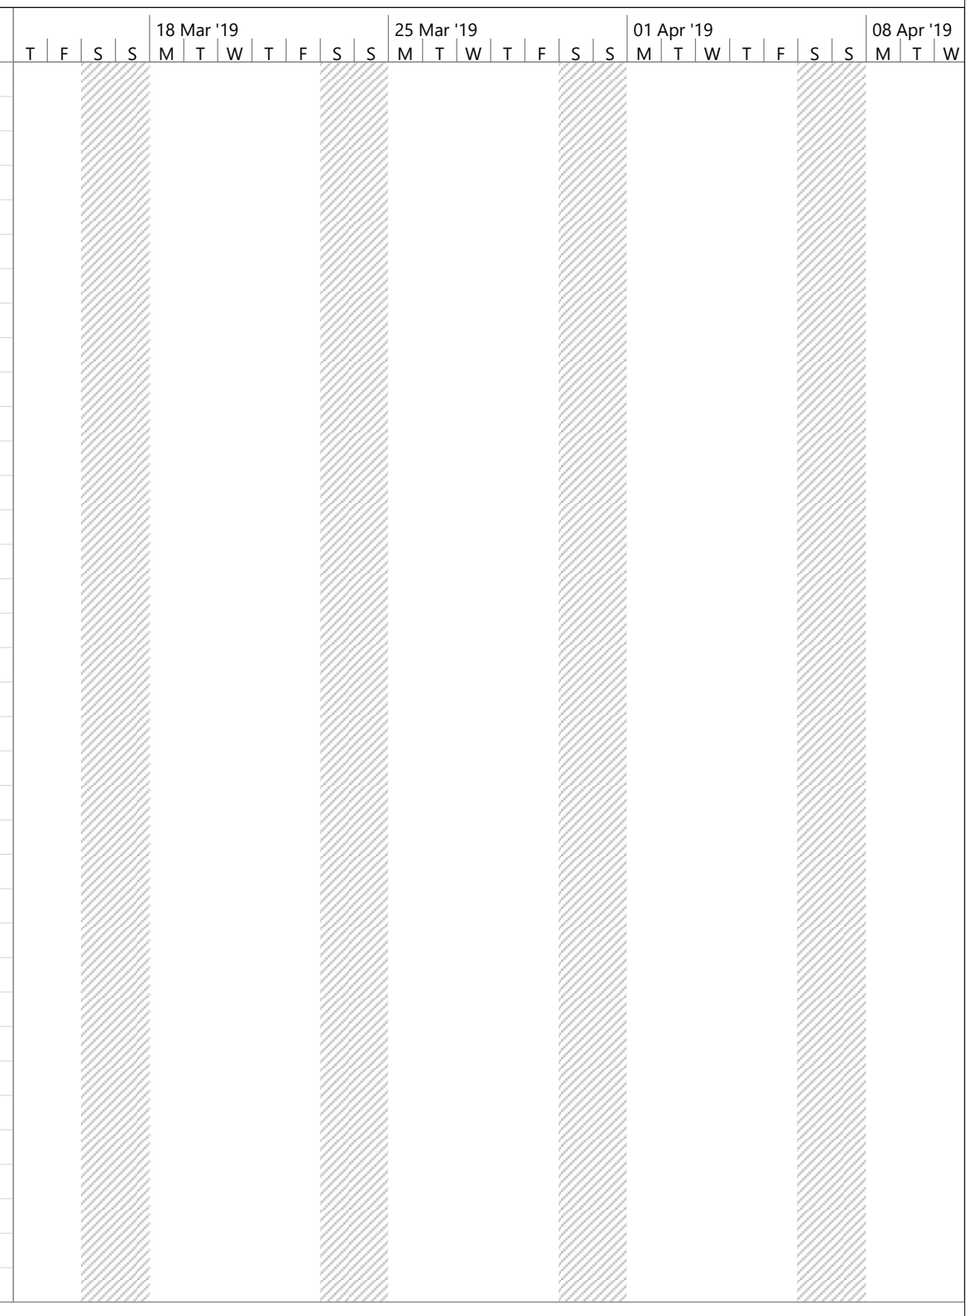

Programme

Greyline
Taking care of homes

| 19 | | | | | 15 Apr '19 | | | | | | | 22 Apr '19 | | | | | | | 29 Apr '19 | | | | | | | 06 May '19 | | | | | | | 13 May '19 | | | | | | | 20 May '19 | | | | | | | 27 May '19 | | | | | | | 03 Jun '19 | | | | | | | 10 Jun '19 | | | | | | | 17 Jun '19 | | | |
|---|---|---

Programme

Greyline
Taking care of homes

| F | S | S | 24 Jun '19 M | T | W | T | F | S | S | 01 Jul '19 M | T | W | T | F | S | S | 08 Jul '19 M | T | W | T | F | S | S | 15 Jul '19 M | T | W | T | F | S | S | 22 Jul '19 M | T | W | T | F | S | S | 29 Jul '19 M | T | W | T | F | S | S | 05 Aug '19 M | T | W | T | F | S | S | 12 Aug '19 M | T | W | T | F | S | S | 19 Aug '19 M | T | W | T | F | S | S | 26 Aug '19 M | T | W | T | F | S |
|---|---|---

Programme

Greyline
Taking care of homes

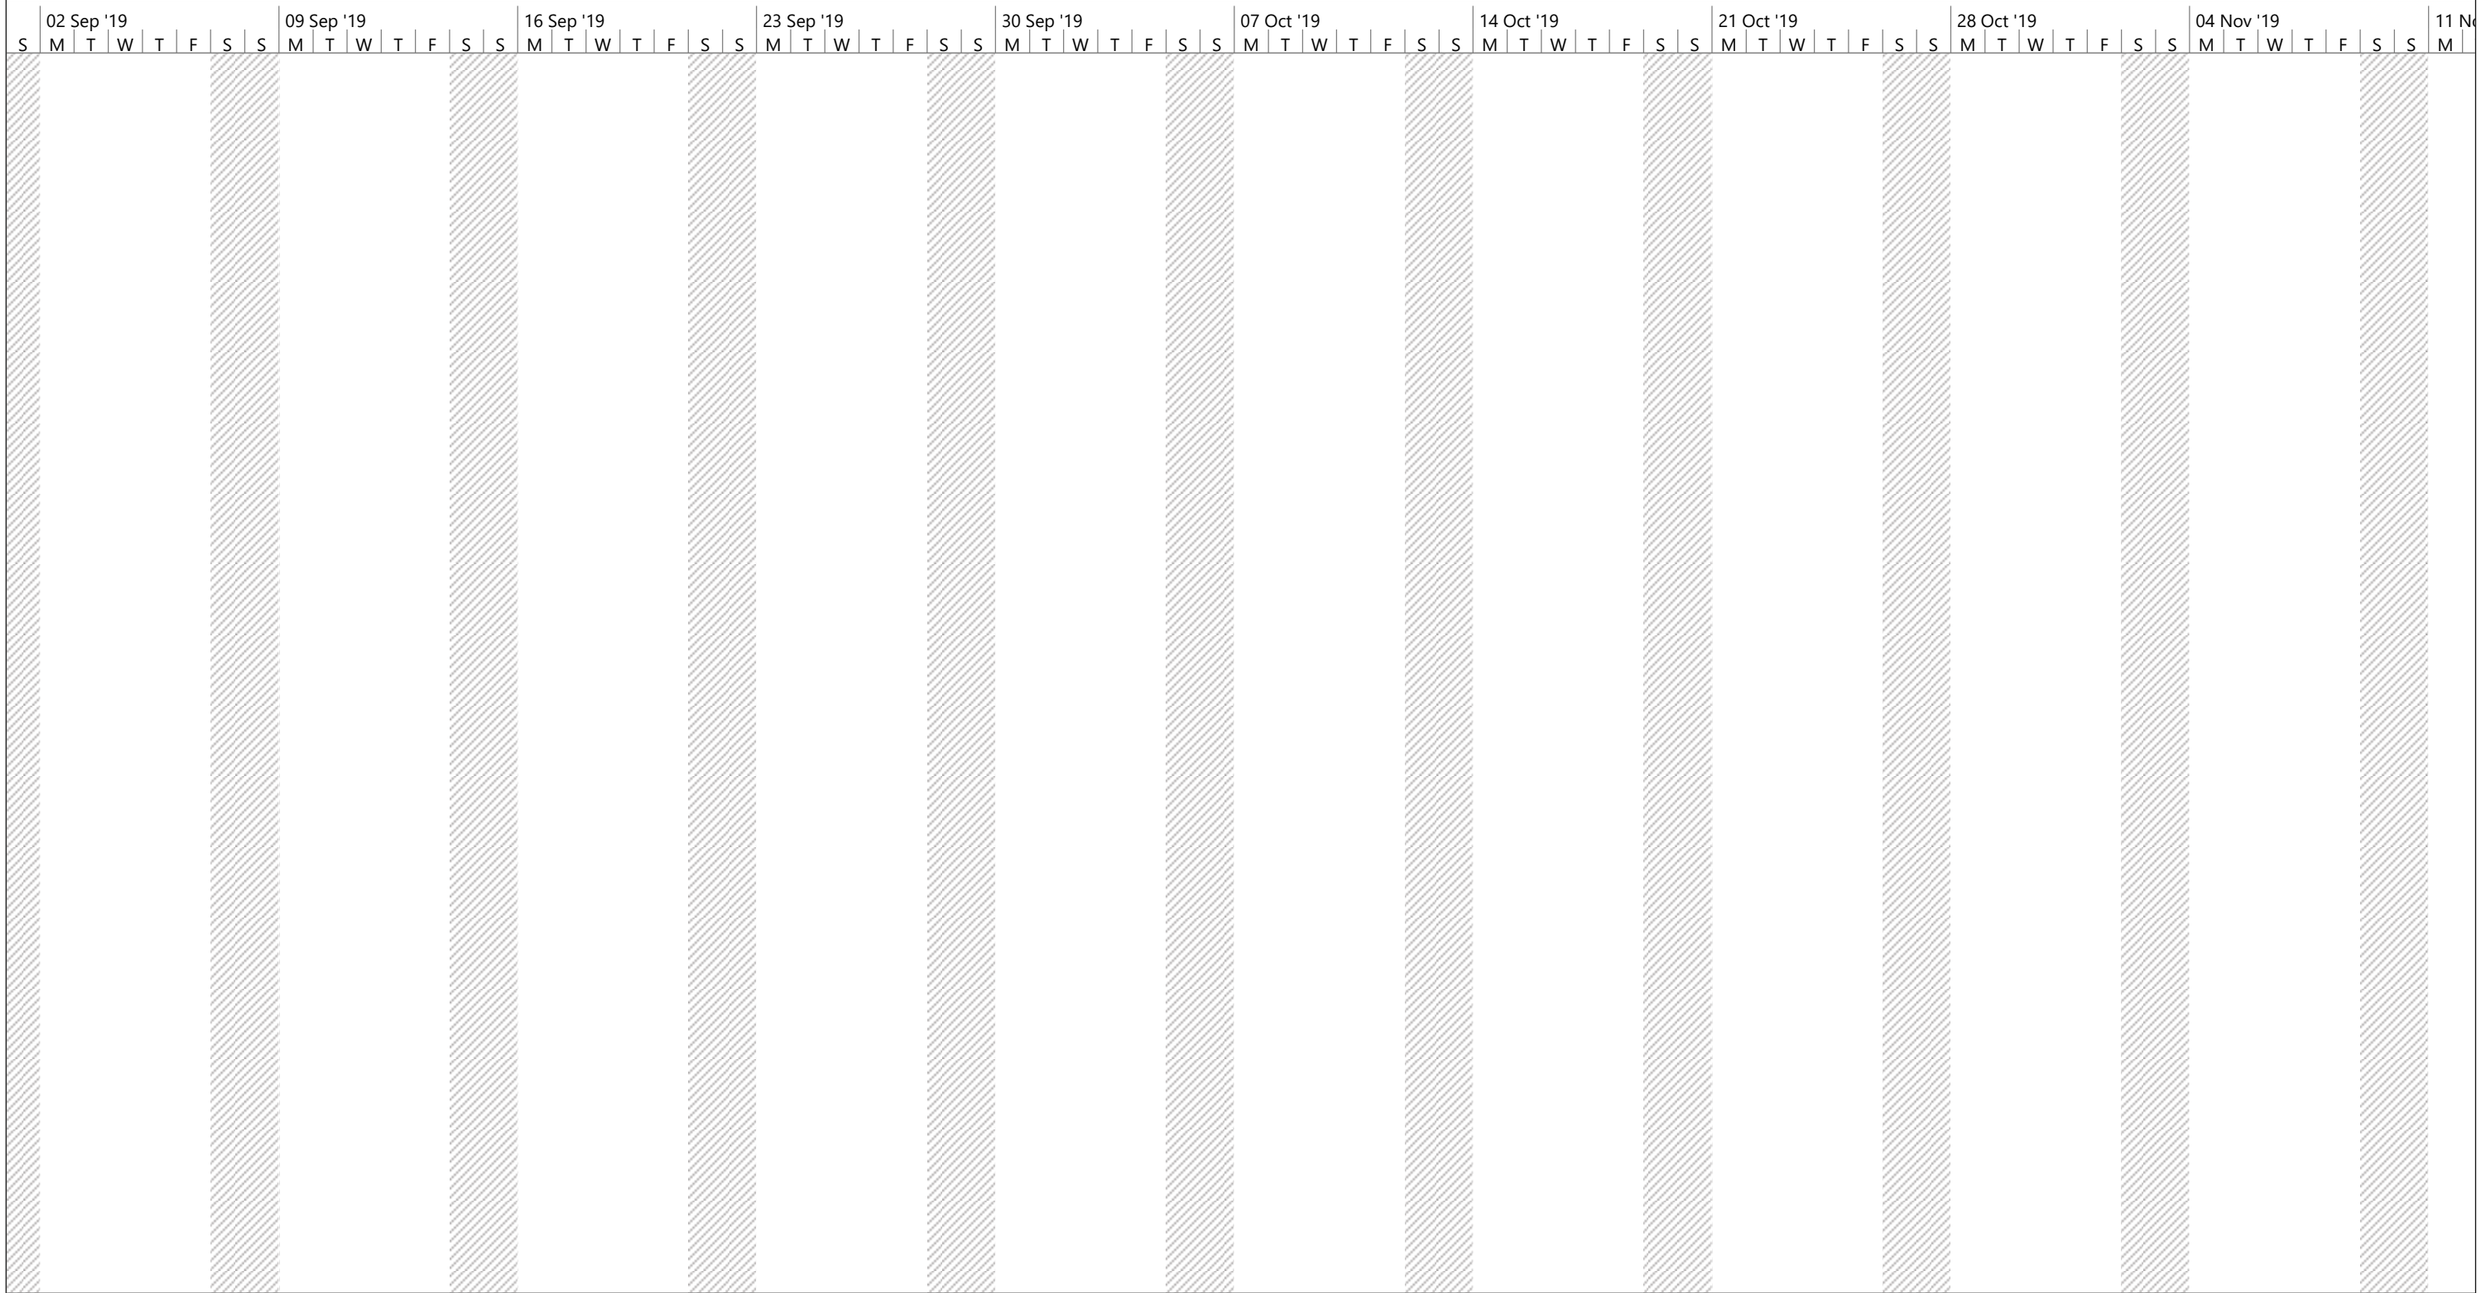

Programme

Greyline
Taking care of homes

| Nov '19 | | | | | | | 18 Nov '19 | | | | | | | 25 Nov '19 | | | | | | | 02 Dec '19 | | | | | | | 09 Dec '19 | | | | | | | 16 Dec '19 | | | | | | | 23 Dec '19 | | | | | | | 30 Dec '19 | | | | | | | 06 Jan '20 | | | | | | | 13 Jan '20 | | | | | | | 20 Jan '20 | | |
|---|---|---

Programme

Greyline
Taking care of homes

| T | F | S | S | 27 Jan '20 M | T | W | T | F | S | S | 03 Feb '20 M | T | W | T | F | S | S | 10 Feb '20 M | T | W | T | F | S | S | 17 Feb '20 M | T | W | T | F | S | S | 24 Feb '20 M | T | W | T | F | S | S | 02 Mar '20 M | T | W | T | F | S | S | 09 Mar '20 M | T | W | T | F | S | S | 16 Mar '20 M | T | W | T | F | S | S | 23 Mar '20 M | T | W | T | F | S | S | 30 Mar '20 M | T | W | T | F |
|---|---|---

Programme

Greyline
Taking care of homes

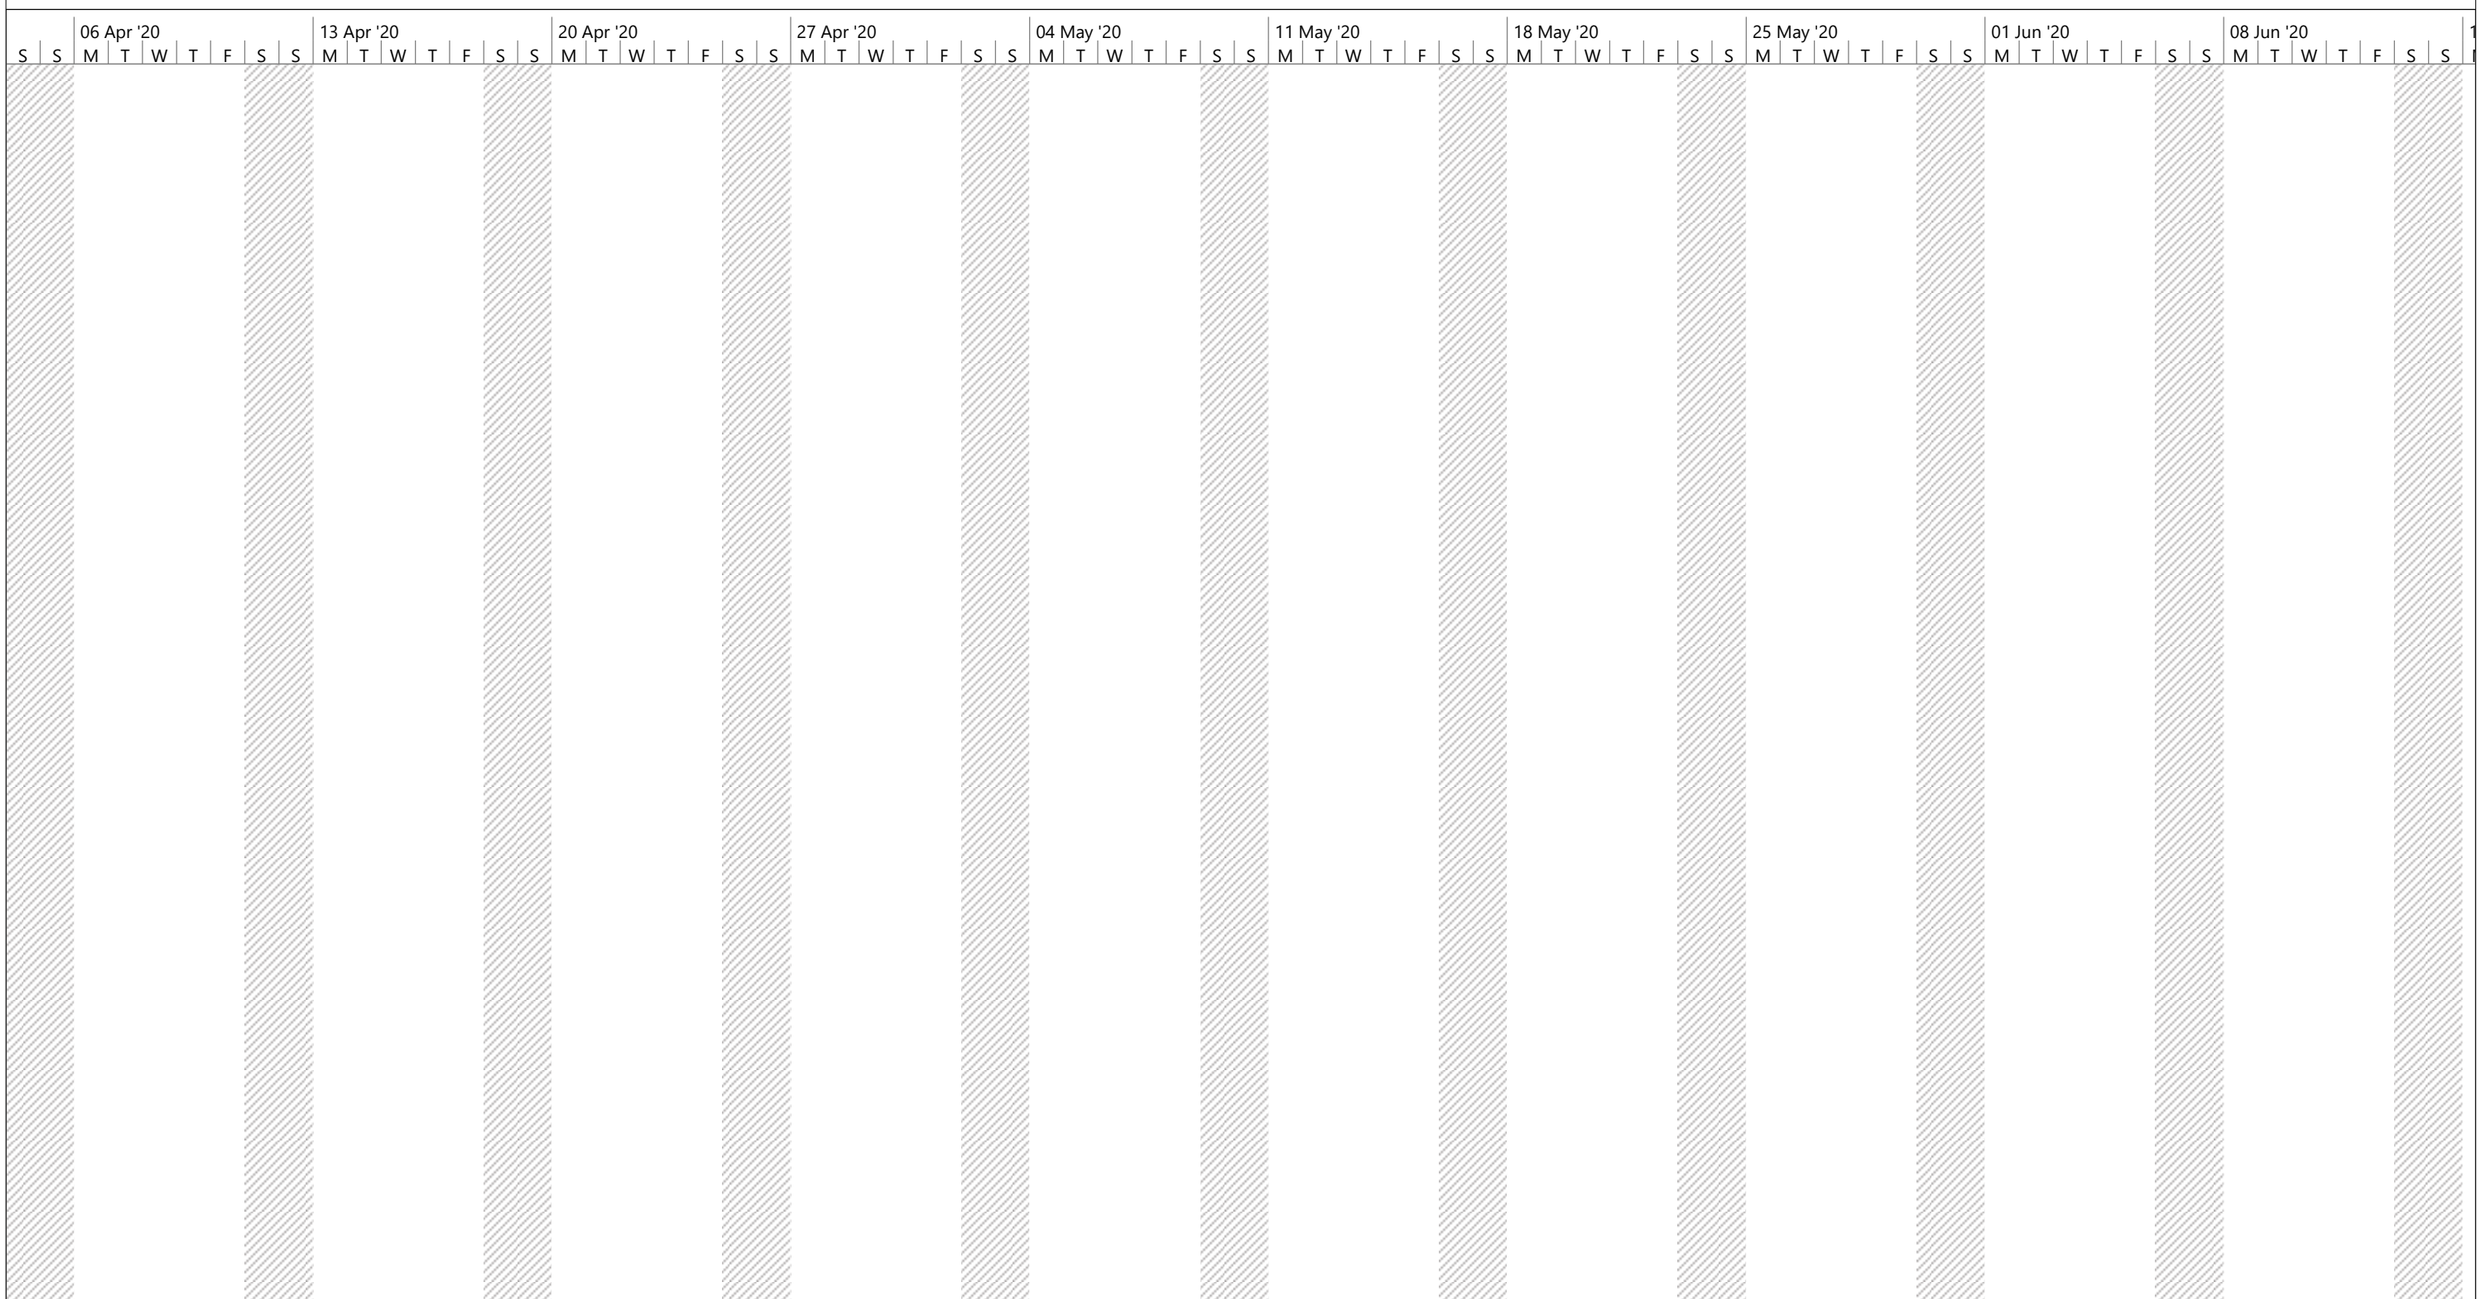

Programme

Greyline
Taking care of homes

| 15 Jun '20 | | | | | | | 22 Jun '20 | | | | | | | 29 Jun '20 | | | | | | | 06 Jul '20 | | | | | | | 13 Jul '20 | | | | | | | 20 Jul '20 | | | | | | | 27 Jul '20 | | | | | | | 03 Aug '20 | | | | | | | 10 Aug '20 | | | | | | | 17 Aug '20 | | | | | | | 24 Aug '2 | |
|---|---|---

Programme

Greyline
Taking care of homes

'20 W T F S S | 31 Aug '20 M T W T F S S | 07 Sep '20 M T W T F S S | 14 Sep '20 M T W T F S S | 21 Sep '20 M T W T F S S | 28 Sep '20 M T W T F S S | 05 Oct '20 M T W T F S S | 12 Oct '20 M T W T F S S | 19 Oct '20 M T W T F S S | 26 Oct '20 M T W T F S S | 02 Nov '20 M T W T

Programme

Greyline
Taking care of homes

Programme

Greyline
Taking care of homes

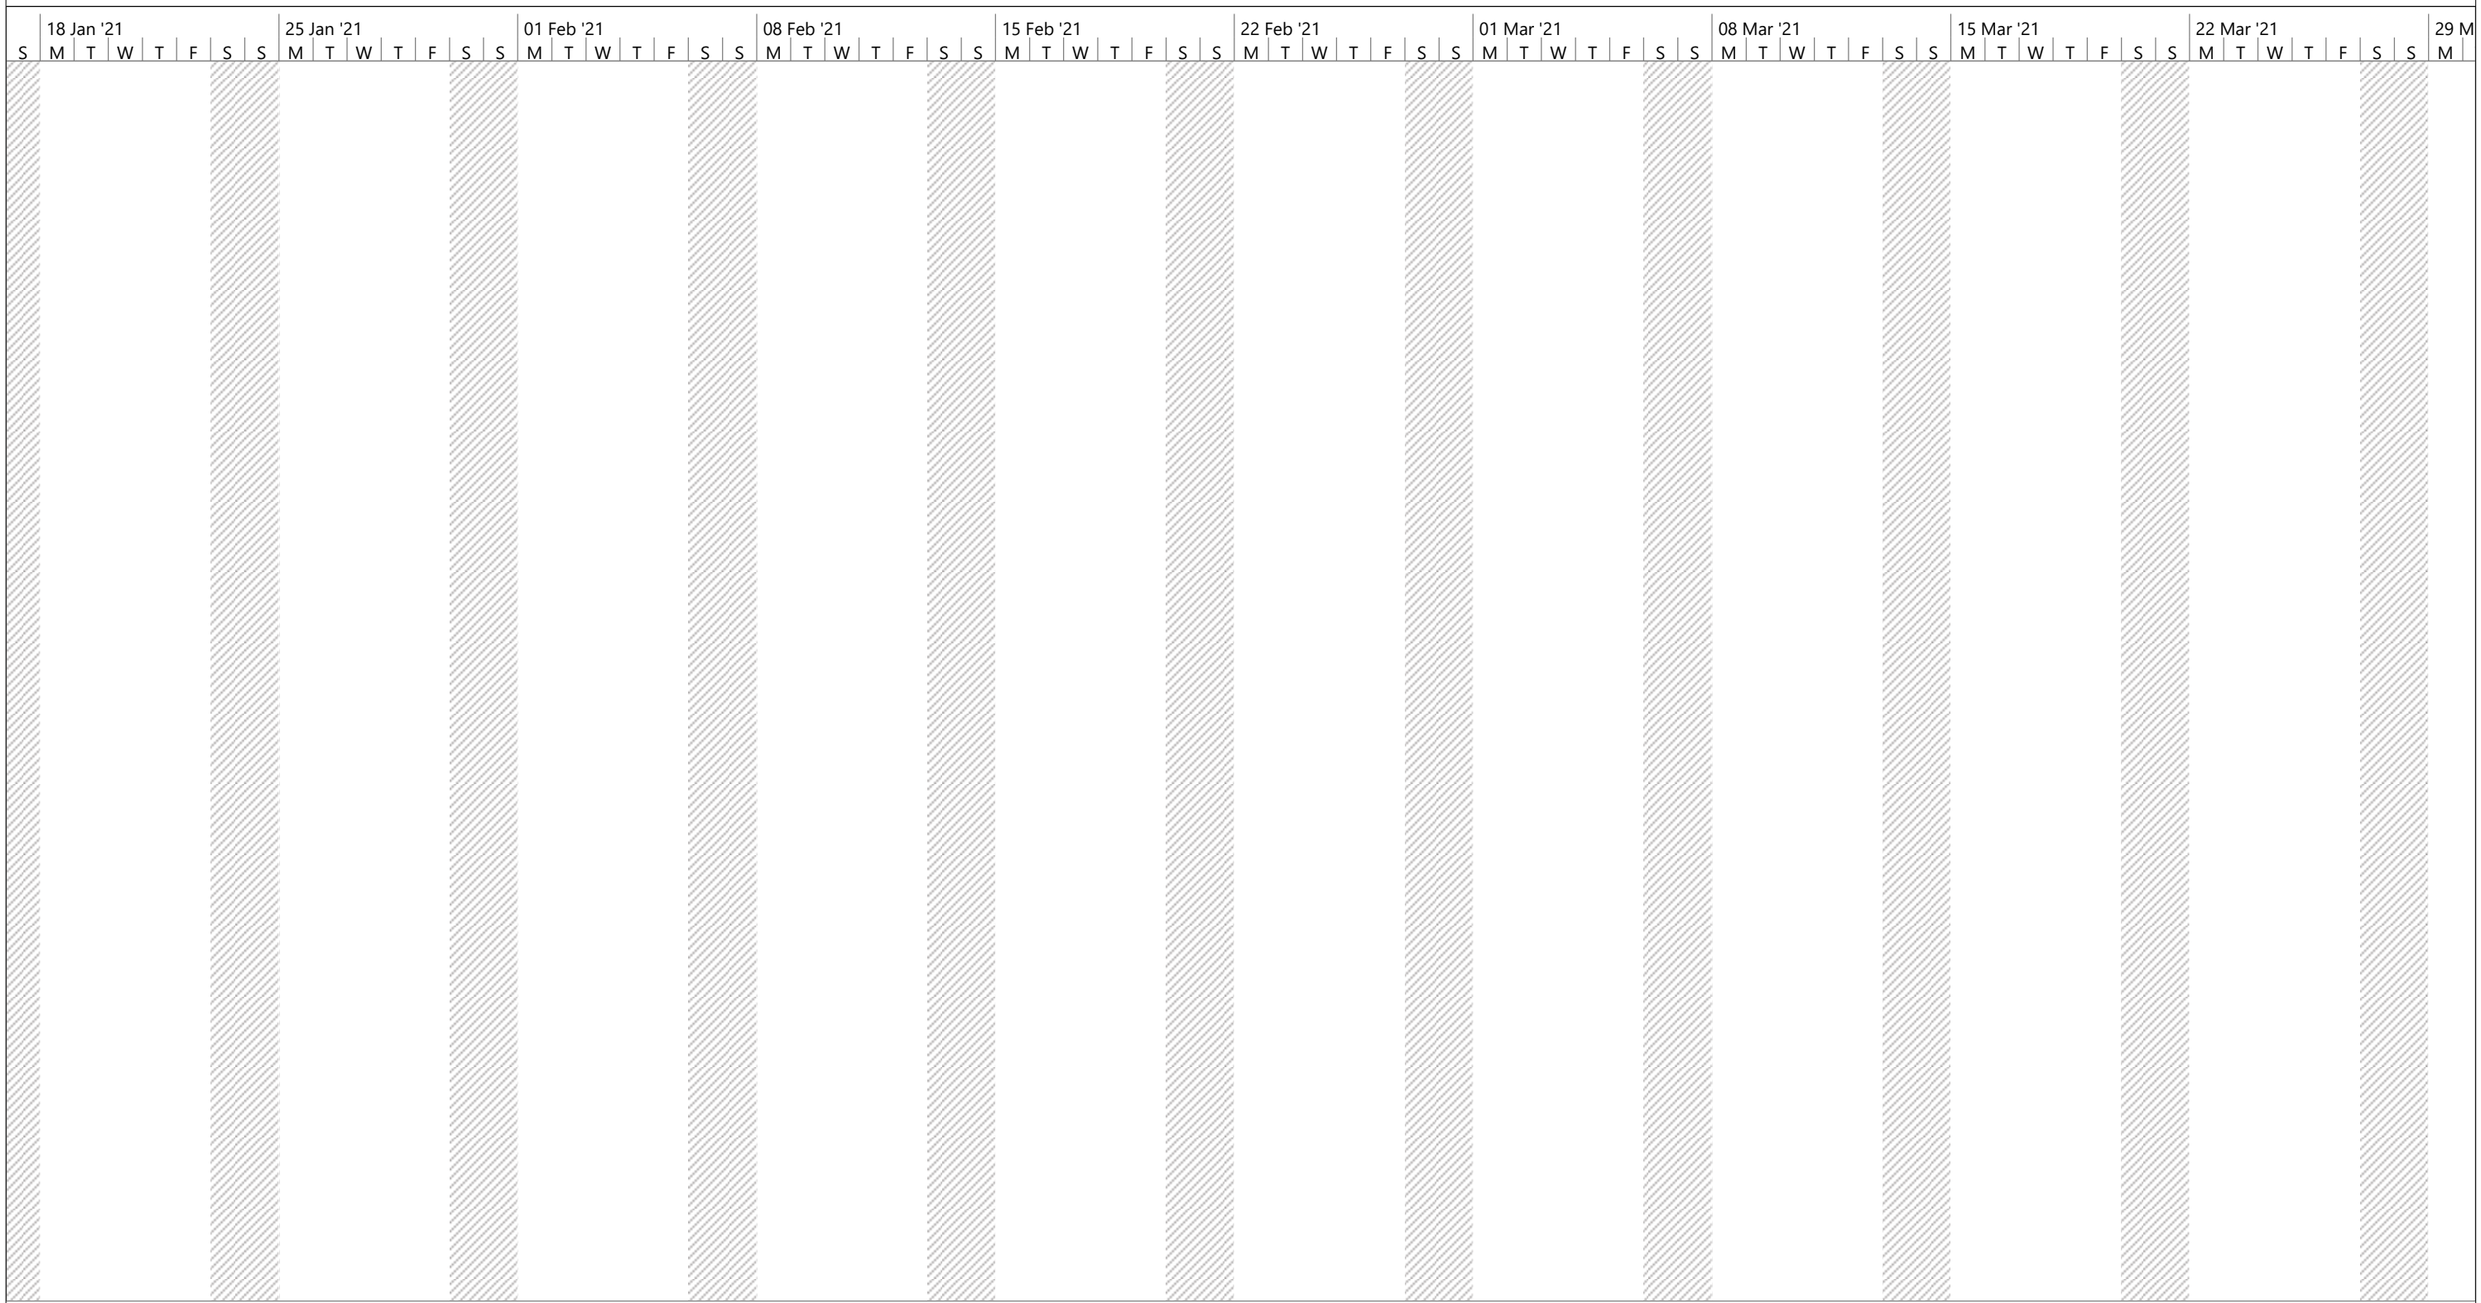

Programme

Greyline
Taking care of homes

| Mar '21 | | | | | | | 05 Apr '21 | | | | | | | 12 Apr '21 | | | | | | | 19 Apr '21 | | | | | | | 26 Apr '21 | | | | | | | 03 May '21 | | | | | | | 10 May '21 | | | | | | | 17 May '21 | | | | | | | 24 May '21 | | | | | | | 31 May '21 | | | | | | | 07 Jun '21 | | |
|---|---|---

Programme

Greyline
Taking care of homes

| T | F | S | S | 14 Jun '21 M | T | W | T | F | S | S | 21 Jun '21 M | T | W | T | F | S | S | 28 Jun '21 M | T | W | T | F | S | S | 05 Jul '21 M | T | W | T | F | S | S | 12 Jul '21 M | T | W | T | F | S | S | 19 Jul '21 M | T | W | T | F | S | S | 26 Jul '21 M | T | W | T | F | S | S | 02 Aug '21 M | T | W | T | F | S | S | 09 Aug '21 M | T | W | T | F | S | S | 16 Aug '21 M | T | W | T | F |
|---|---|---

Programme

Greyline
Taking care of homes

S	S	23 Aug '21 M	T	W	T	F	S	S	30 Aug '21 M	T	W	T	F	S	S	06 Sep '21 M	T	W	T	F	S	S	13 Sep '21 M	T	W	T	F	S	S	20 Sep '21 M	T	W	T	F	S	S	27 Sep '21 M	T	W	T	F	S	S	04 Oct '21 M	T	W	T	F	S	S	11 Oct '21 M	T	W	T	F	S	S	18 Oct '21 M	T	W	T	F	S	S	25 Oct '21 M	T	W	T	F	S	S

Programme

Greyline
Taking care of homes

| 01 Nov '21 | | | | | | | 08 Nov '21 | | | | | | | 15 Nov '21 | | | | | | | 22 Nov '21 | | | | | | | 29 Nov '21 | | | | | | | 06 Dec '21 | | | | | | | 13 Dec '21 | | | | | | | 20 Dec '21 | | | | | | | 27 Dec '21 | | | | | | | 03 Jan '22 | | | | | | | 10 Jan '22 |
|---|---|---

Programme

Greyline
Taking care of homes

22 W T F S S | 17 Jan '22 M T W T F S S | 24 Jan '22 M T W T F S S | 31 Jan '22 M T W T F S S | 07 Feb '22 M T W T F S S | 14 Feb '22 M T W T F S S | 21 Feb '22 M T W T F S S | 28 Feb '22 M T W T F S S | 07 Mar '22 M T W T F S S | 14 Mar '22 M T W T F S S | 21 Mar '22 M T W T

Programme

Greyline
Taking care of homes

| F | S | S | 28 Mar '22 M | T | W | T | F | S | S | 04 Apr '22 M | T | W | T | F | S | S | 11 Apr '22 M | T | W | T | F | S | S | 18 Apr '22 M | T | W | T | F | S | S | 25 Apr '22 M | T | W | T | F | S | S | 02 May '22 M | T | W | T | F | S | S | 09 May '22 M | T | W | T | F | S | S | 16 May '22 M | T | W | T | F | S | S | 23 May '22 M | T | W | T | F | S | S | 30 May '22 M | T | W | T | F | S |
|---|---|---

Programme

Greyline
Taking care of homes

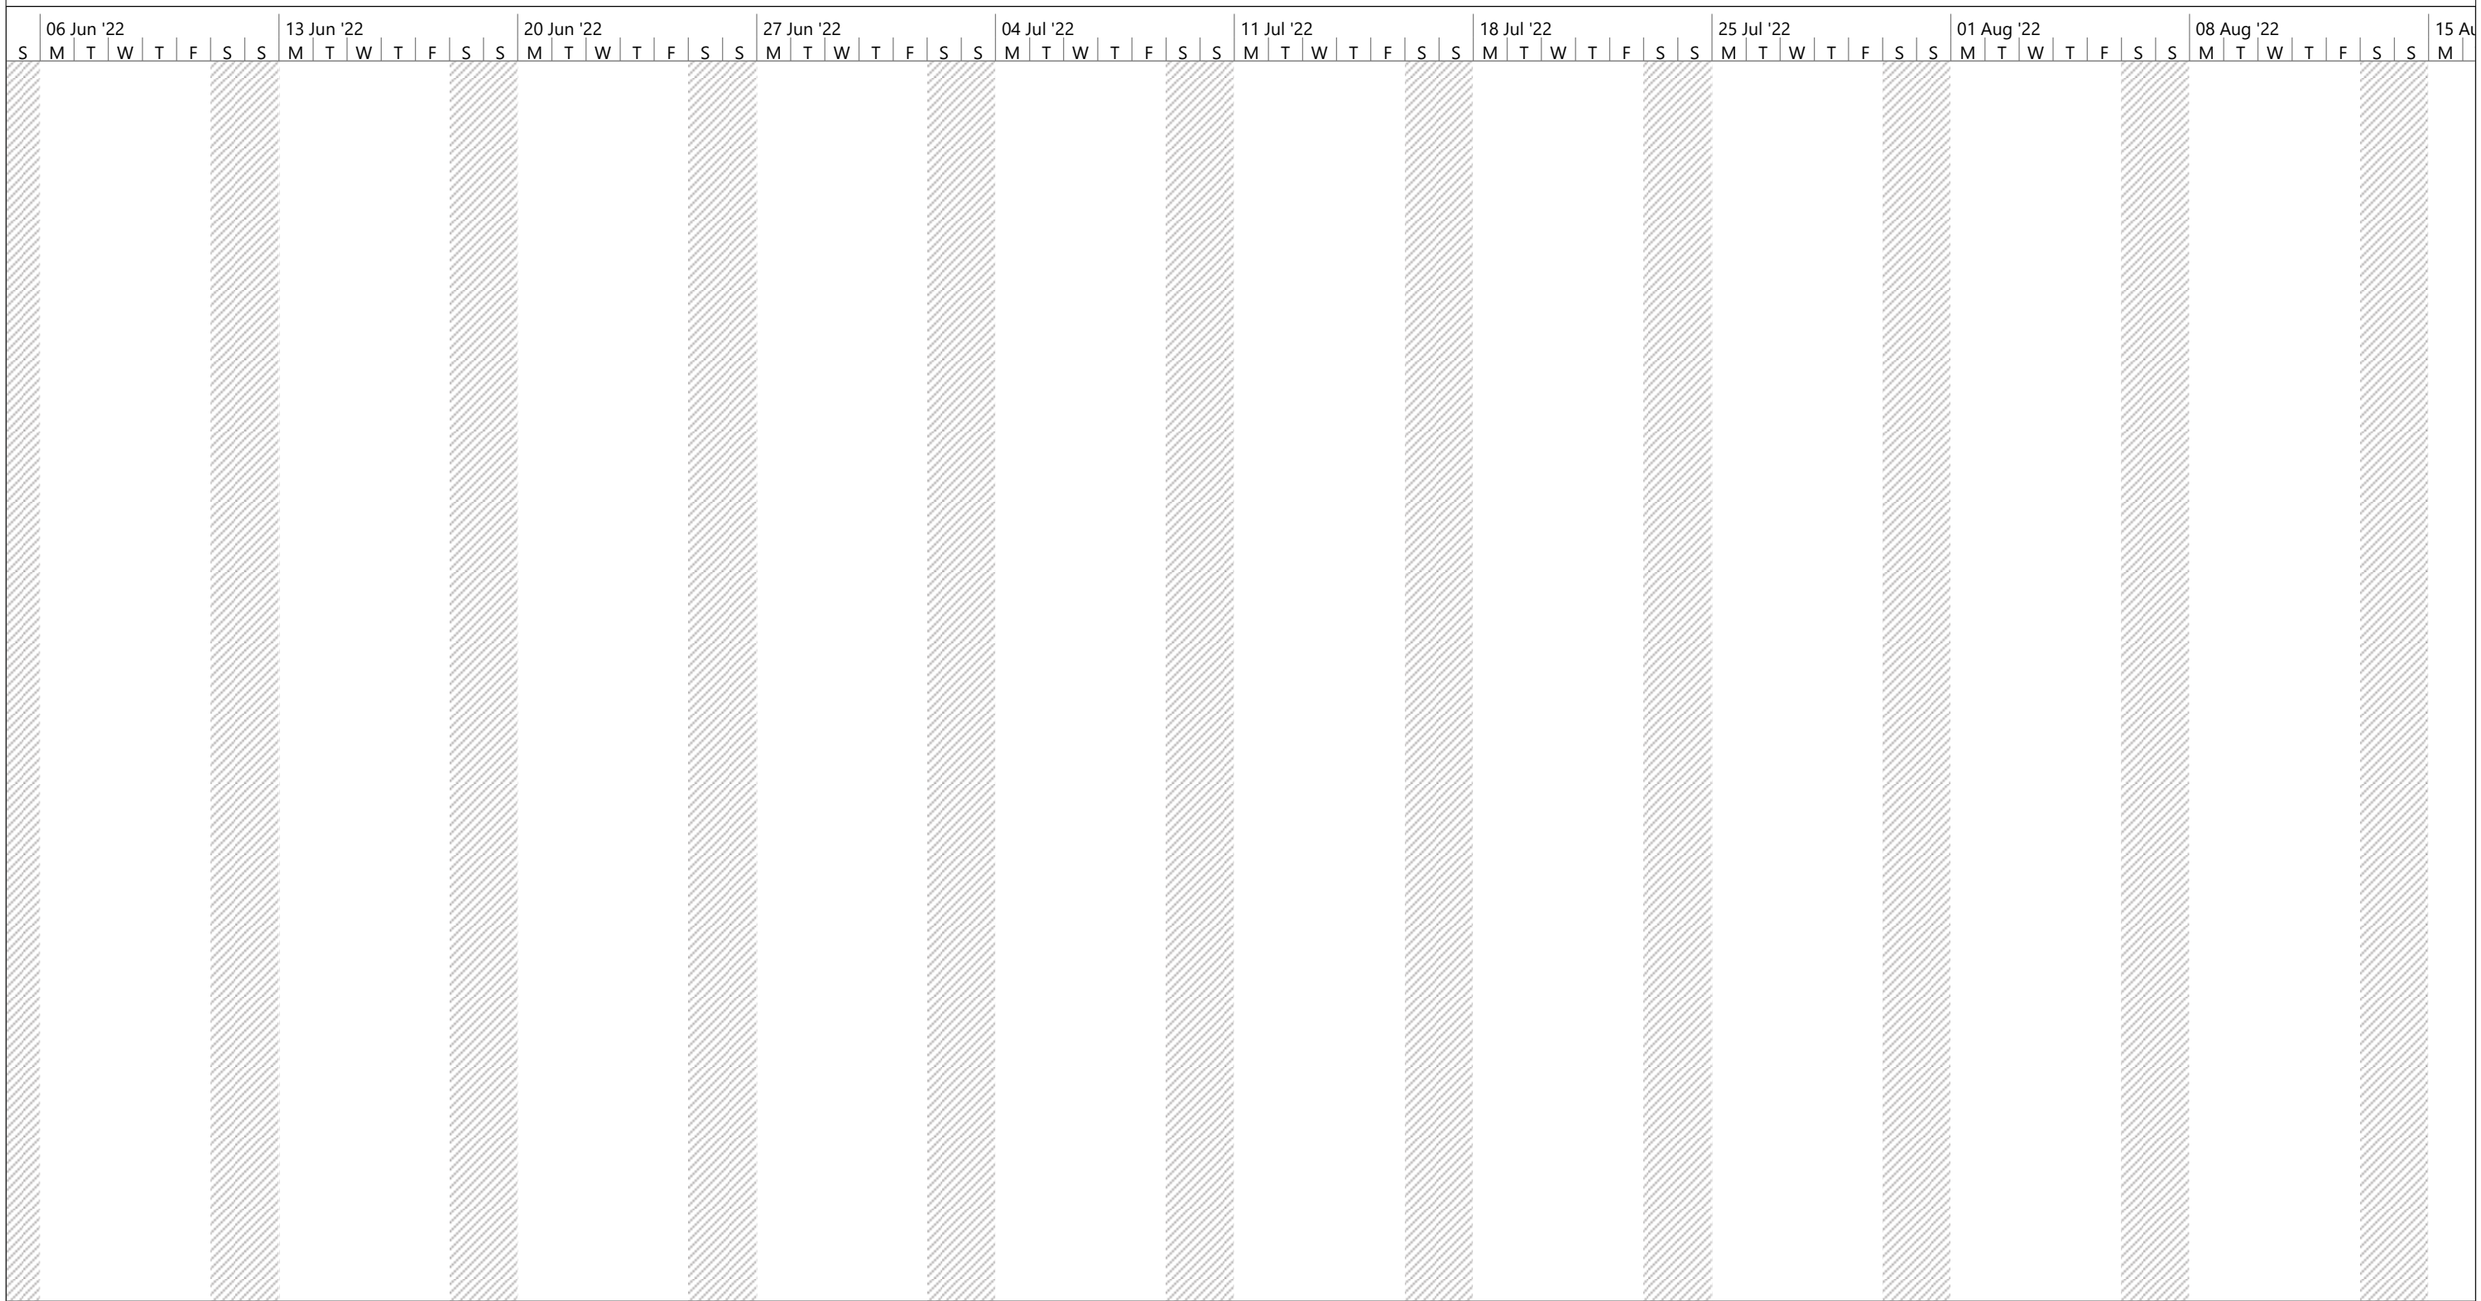

Programme

Greyline
Taking care of homes

| Aug '22 | | | | | | | 22 Aug '22 | | | | | | | 29 Aug '22 | | | | | | | 05 Sep '22 | | | | | | | 12 Sep '22 | | | | | | | 19 Sep '22 | | | | | | | 26 Sep '22 | | | | | | | 03 Oct '22 | | | | | | | 10 Oct '22 | | | | | | | 17 Oct '22 | | | | | | | 24 Oct '22 | | |
|---|---|---

Programme

Greyline
Taking care of homes

T	F	S	S	31 Oct '22 M	T	W	T	F	S	S	07 Nov '22 M	T	W	T	F	S	S	14 Nov '22 M	T	W	T	F	S	S	21 Nov '22 M	T	W	T	F	S	S	28 Nov '22 M	T	W	T	F	S	S	05 Dec '22 M	T	W	T	F	S	S	12 Dec '22 M	T	W	T	F	S	S	19 Dec '22 M	T	W	T	F	S	S	26 Dec '22 M	T	W	T	F	S	S	02 Jan '23 M	T	W	T	F

Programme

Greyline
Taking care of homes

S	S	09 Jan '23 M	T	W	T	F	S	S	16 Jan '23 M	T	W	T	F	S	S	23 Jan '23 M	T	W	T	F	S	S	30 Jan '23 M	T	W	T	F	S	S	06 Feb '23 M	T	W	T	F	S	S	13 Feb '23 M	T	W	T	F	S	S	20 Feb '23 M	T	W	T	F	S	S	27 Feb '23 M	T	W	T	F	S	S	06 Mar '23 M	T	W	T	F	S	S	13 Mar '23 M	T	W	T	F	S	S	2

Programme

Greyline
Taking care of homes

| 20 Mar '23 | | | | | | | 27 Mar '23 | | | | | | | 03 Apr '23 | | | | | | | 10 Apr '23 | | | | | | | 17 Apr '23 | | | | | | | 24 Apr '23 | | | | | | | 01 May '23 | | | | | | | 08 May '23 | | | | | | | 15 May '23 | | | | | | | 22 May '23 | | | | | | | 29 May '2 | |
|---|---|---

Programme

Greyline
Taking care of homes

'23 W T F S S | 05 Jun '23 M T W T F S S | 12 Jun '23 M T W T F S S | 19 Jun '23 M T W T F S S | 26 Jun '23 M T W T F S S | 03 Jul '23 M T W T F S S | 10 Jul '23 M T W T F S S | 17 Jul '23 M T W T F S S | 24 Jul '23 M T W T F S S | 31 Jul '23 M T W T F S S | 07 Aug '23 M T W T

Programme

Greyline
Taking care of homes

| F | S | S | 14 Aug '23 M | T | W | T | F | S | S | 21 Aug '23 M | T | W | T | F | S | S | 28 Aug '23 M | T | W | T | F | S | S | 04 Sep '23 M | T | W | T | F | S | S | 11 Sep '23 M | T | W | T | F | S | S | 18 Sep '23 M | T | W | T | F | S | S | 25 Sep '23 M | T | W | T | F | S | S | 02 Oct '23 M | T | W | T | F | S | S | 09 Oct '23 M | T | W | T | F | S | S | 16 Oct '23 M | T | W | T | F | S |
|---|---|---

Programme

Greyline
Taking care of homes

| S | 23 Oct '23 M | T | W | T | F | S | S | 30 Oct '23 M | T | W | T | F | S | S | 06 Nov '23 M | T | W | T | F | S | S | 13 Nov '23 M | T | W | T | F | S | S | 20 Nov '23 M | T | W | T | F | S | S | 27 Nov '23 M | T | W | T | F | S | S | 04 Dec '23 M | T | W | T | F | S | S | 11 Dec '23 M | T | W | T | F | S | S | 18 Dec '23 M | T | W | T | F | S | S | 25 Dec '23 M | T | W | T | F | S | S | 01 Ja M |
|---|---|---

Programme

Greyline
Taking care of homes

an '24 | 08 Jan '24 | 15 Jan '24 | 22 Jan '24 | 29 Jan '24 | 05 Feb '24 | 12 Feb '24 | 19 Feb '24 | 26 Feb '24 | 04 Mar '24 | 11 Mar '24

T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W

Programme

Greyline
Taking care of homes

T F S S | 18 Mar '24 M T W T F S S | 25 Mar '24 M T W T F S S | 01 Apr '24 M T W T F S S | 08 Apr '24 M T W T F S S | 15 Apr '24 M T W T F S S | 22 Apr '24 M T W T F S S | 29 Apr '24 M T W T F S S | 06 May '24 M T W T F S S | 13 May '24 M T W T F S S | 20 May '24 M T W T F

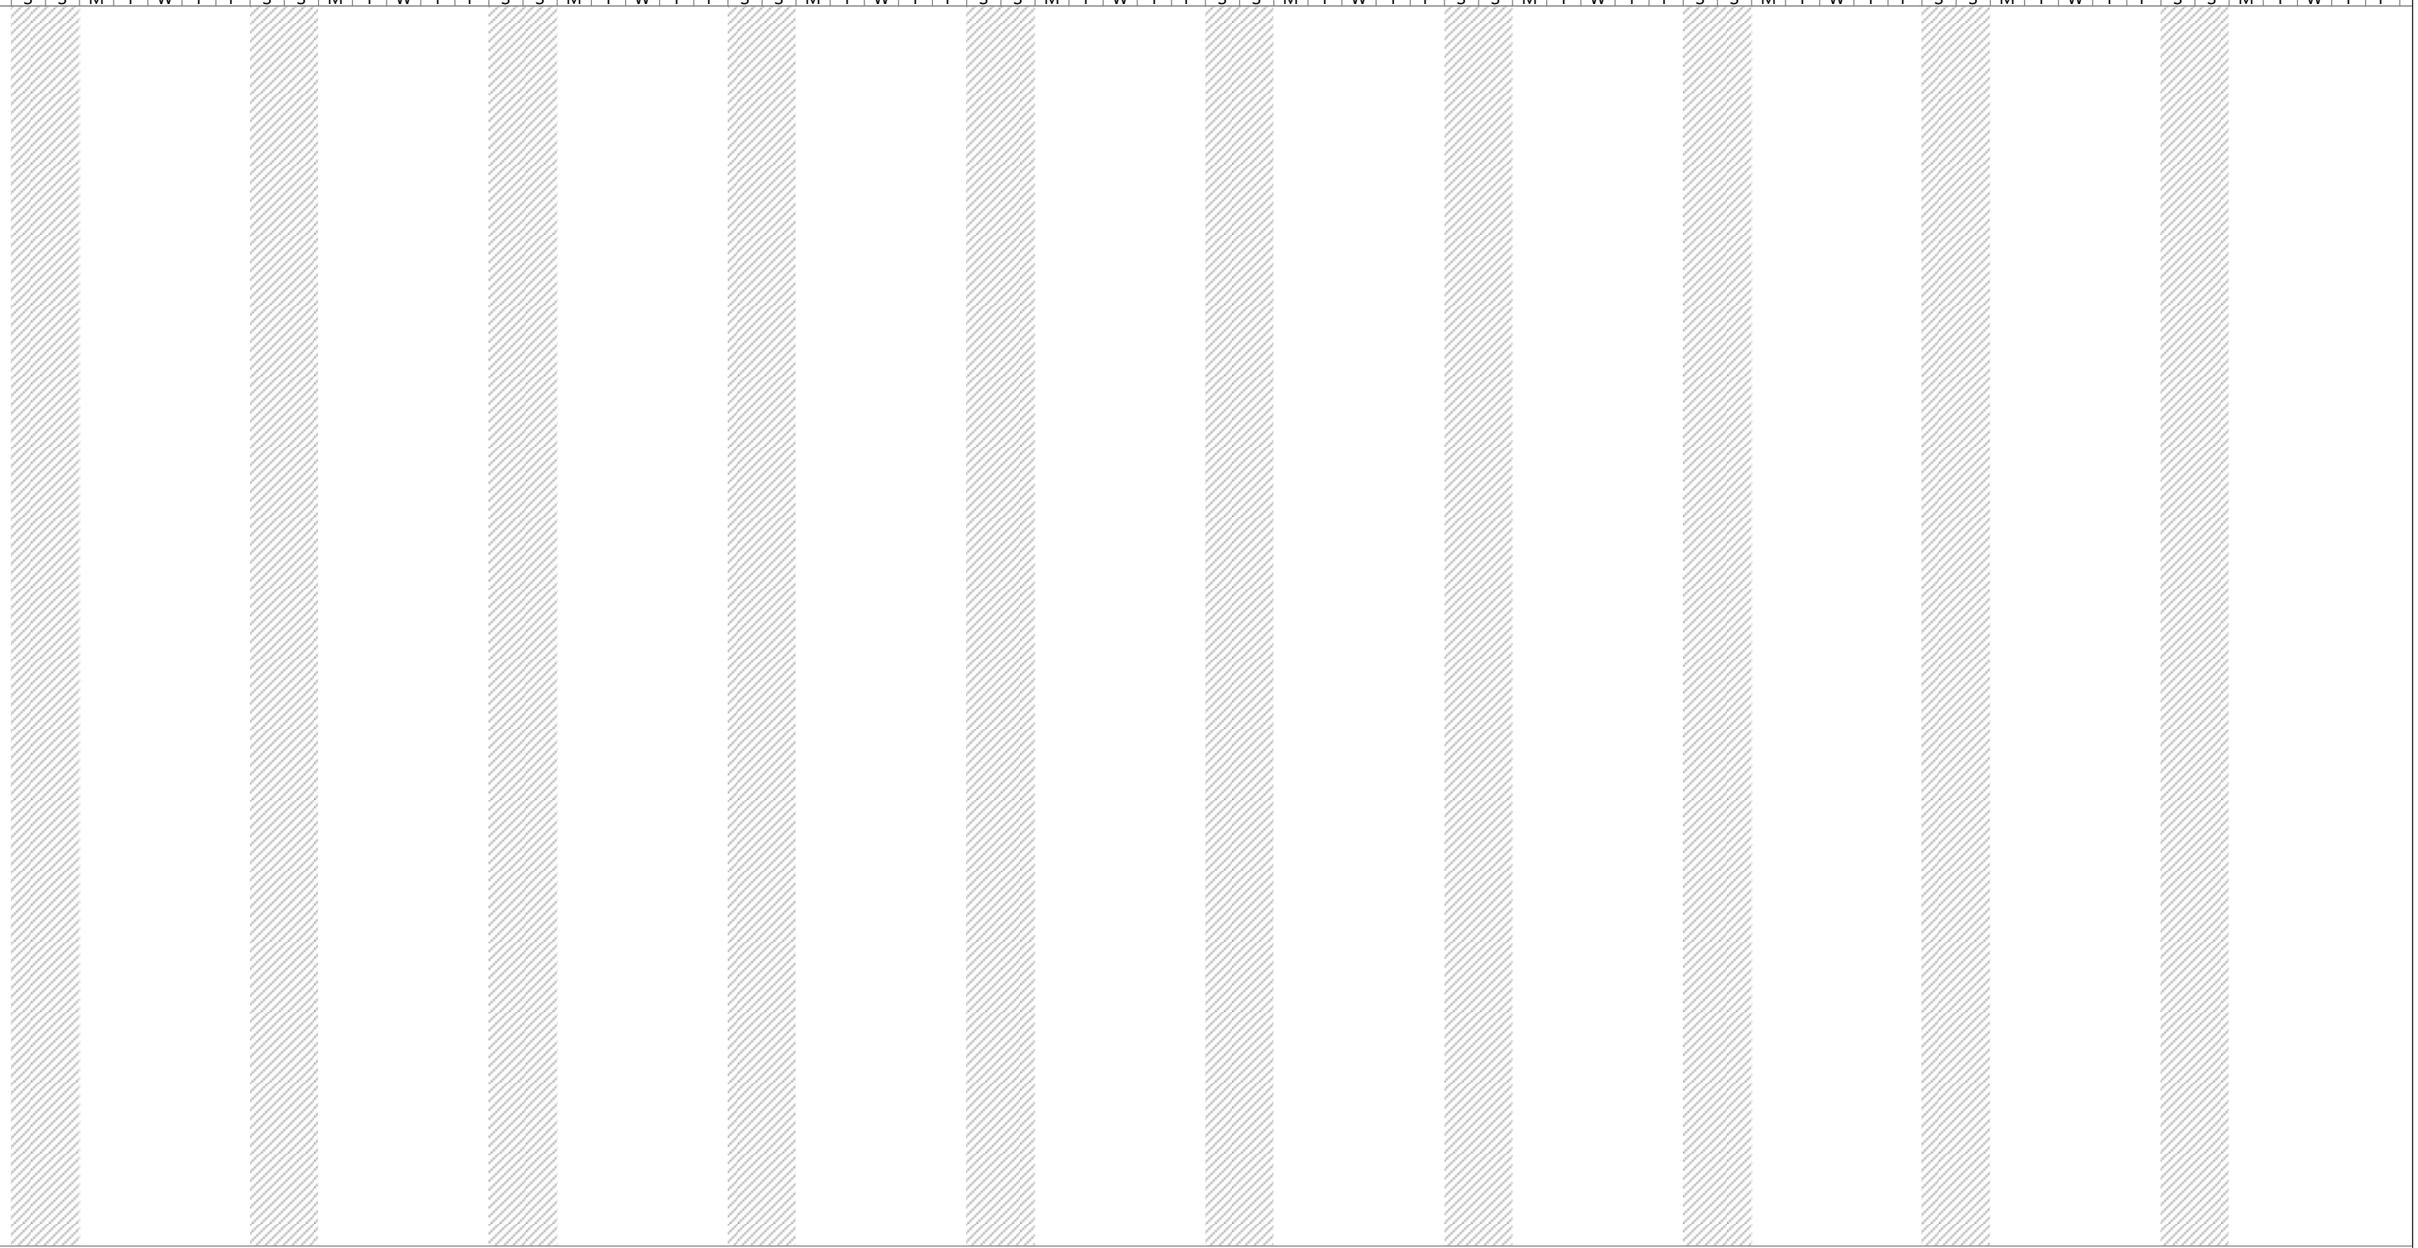

Programme

Greyline
Taking care of homes

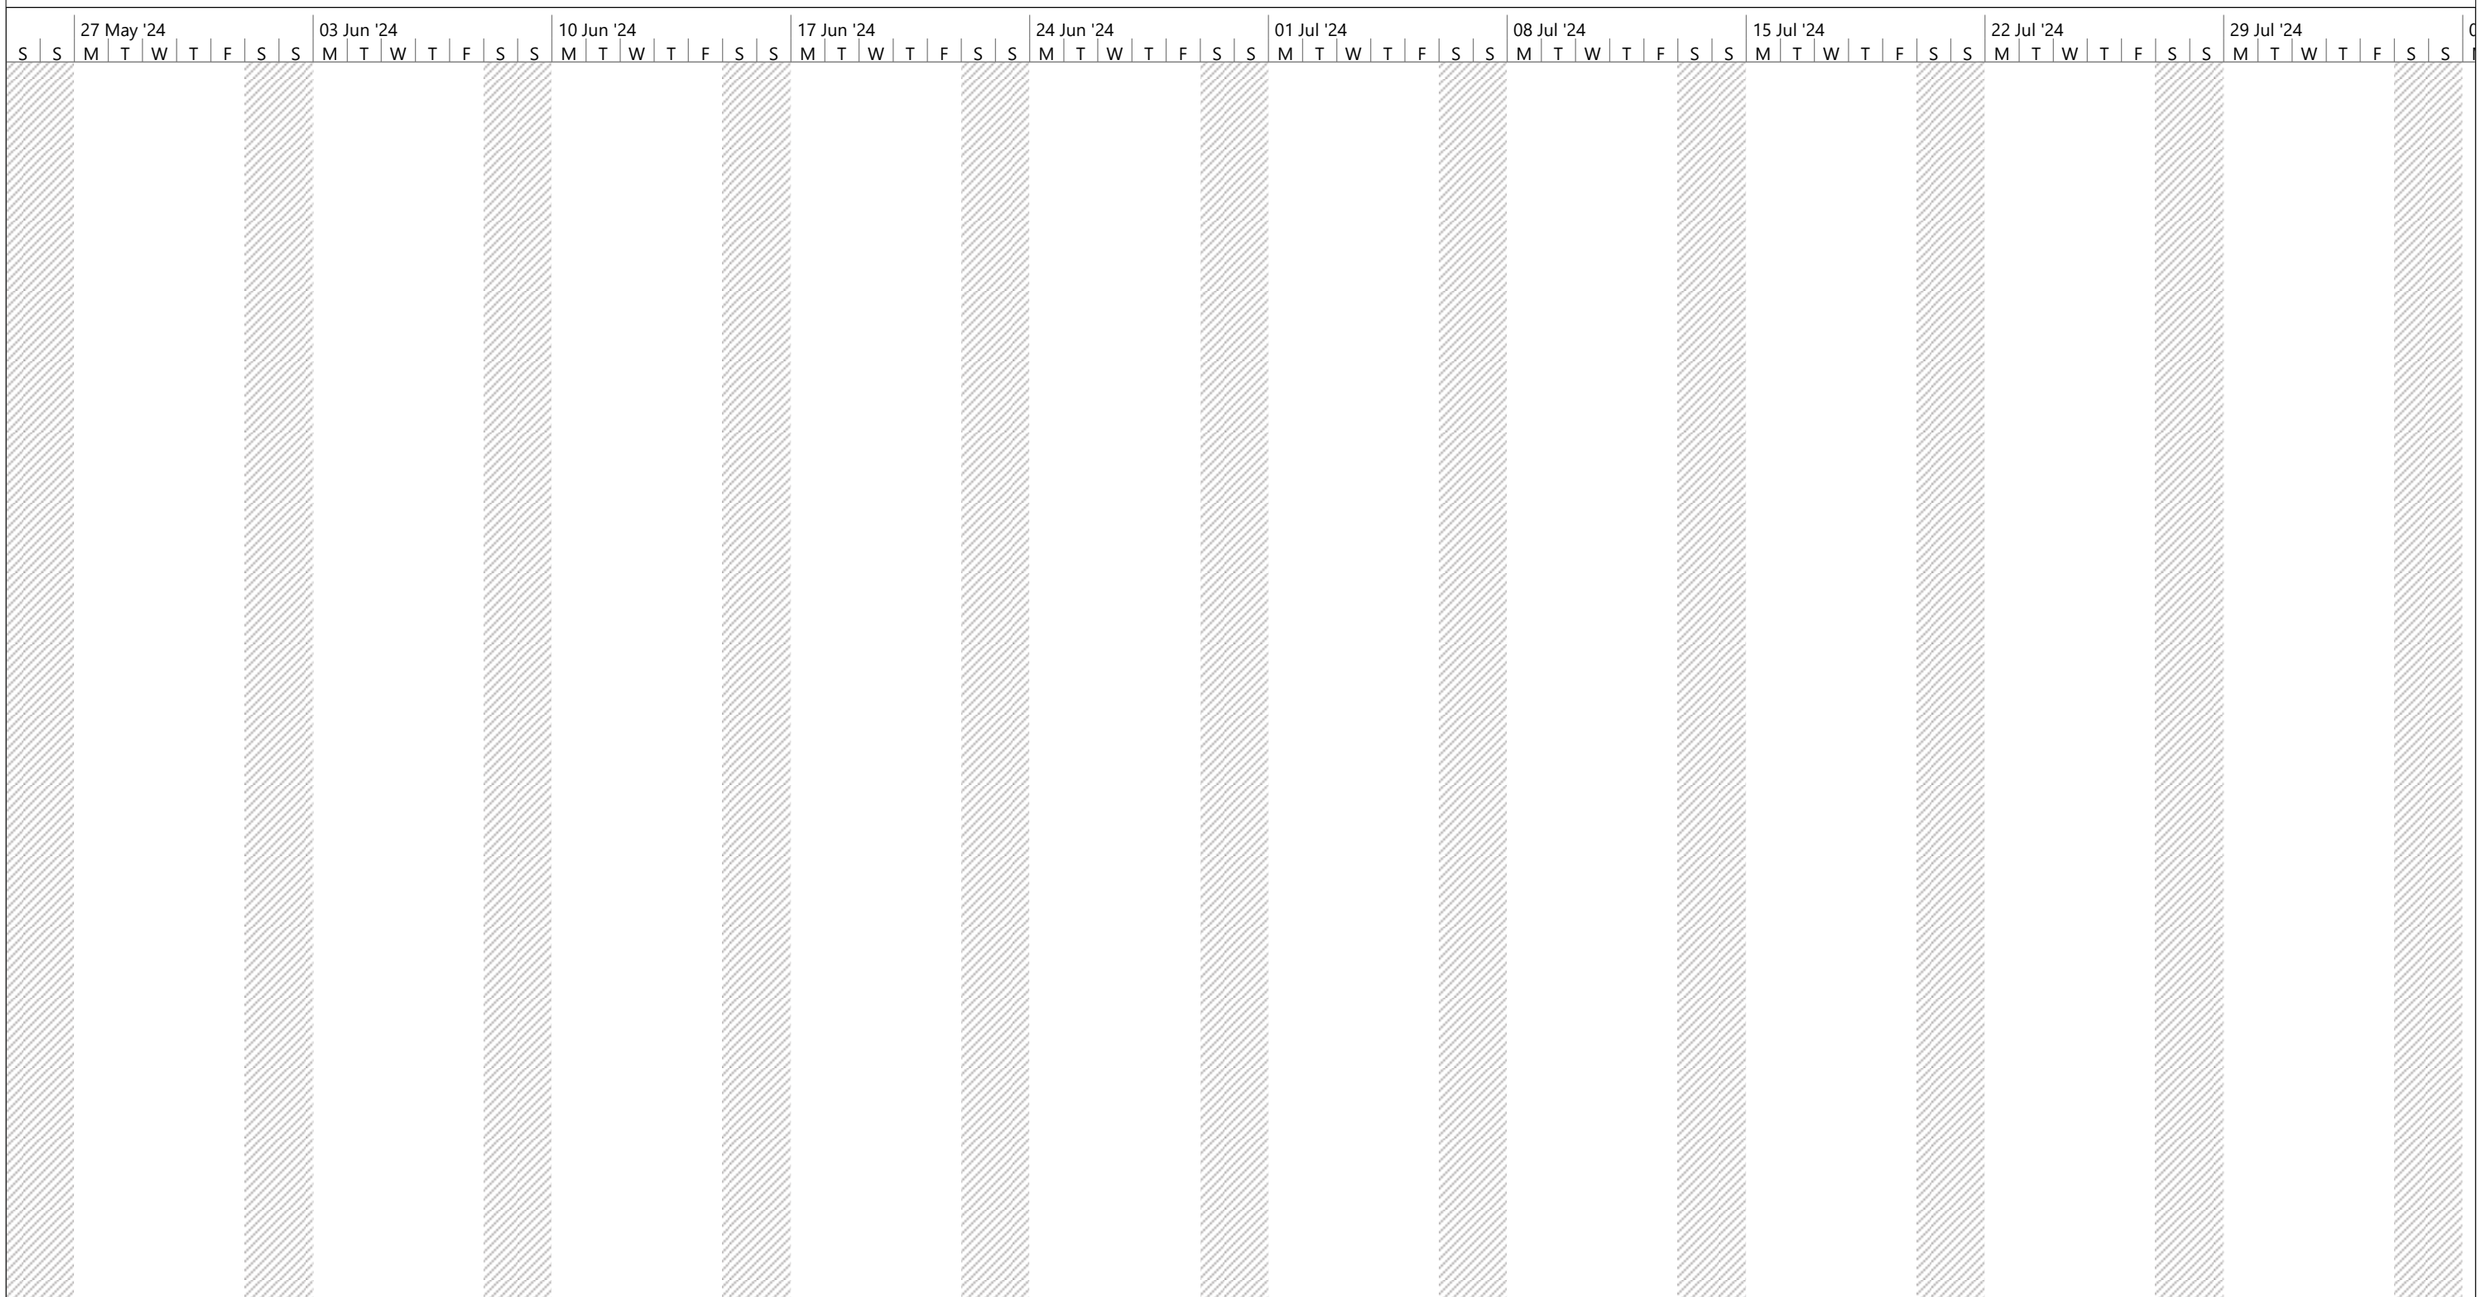

Programme

Greyline
Taking care of homes

| 05 Aug '24 | | | | | | | 12 Aug '24 | | | | | | | 19 Aug '24 | | | | | | | 26 Aug '24 | | | | | | | 02 Sep '24 | | | | | | | 09 Sep '24 | | | | | | | 16 Sep '24 | | | | | | | 23 Sep '24 | | | | | | | 30 Sep '24 | | | | | | | 07 Oct '24 | | | | | | | 14 Oct '24 |
|---|---|---

Programme

Greyline
Taking care of homes

| 24 | | | | | 21 Oct '24 | | | | | | | 28 Oct '24 | | | | | | | 04 Nov '24 | | | | | | | 11 Nov '24 | | | | | | | 18 Nov '24 | | | | | | | 25 Nov '24 | | | | | | | 02 Dec '24 | | | | | | | 09 Dec '24 | | | | | | | 16 Dec '24 | | | | | | | 23 Dec '24 | | | |
|---|---|---

Programme

Greyline
Taking care of homes

| F | S | S | 30 Dec '24 M | T | W | T | F | S | S | 06 Jan '25 M | T | W | T | F | S | S | 13 Jan '25 M | T | W | T | F | S | S | 20 Jan '25 M | T | W | T | F | S | S | 27 Jan '25 M | T | W | T | F | S | S | 03 Feb '25 M | T | W | T | F | S | S | 10 Feb '25 M | T | W | T | F | S | S | 17 Feb '25 M | T | W | T | F | S | S | 24 Feb '25 M | T | W | T | F | S | S | 03 Mar '25 M | T | W | T | F | S |
|---|---|---

Programme

Greyline
Taking care of homes

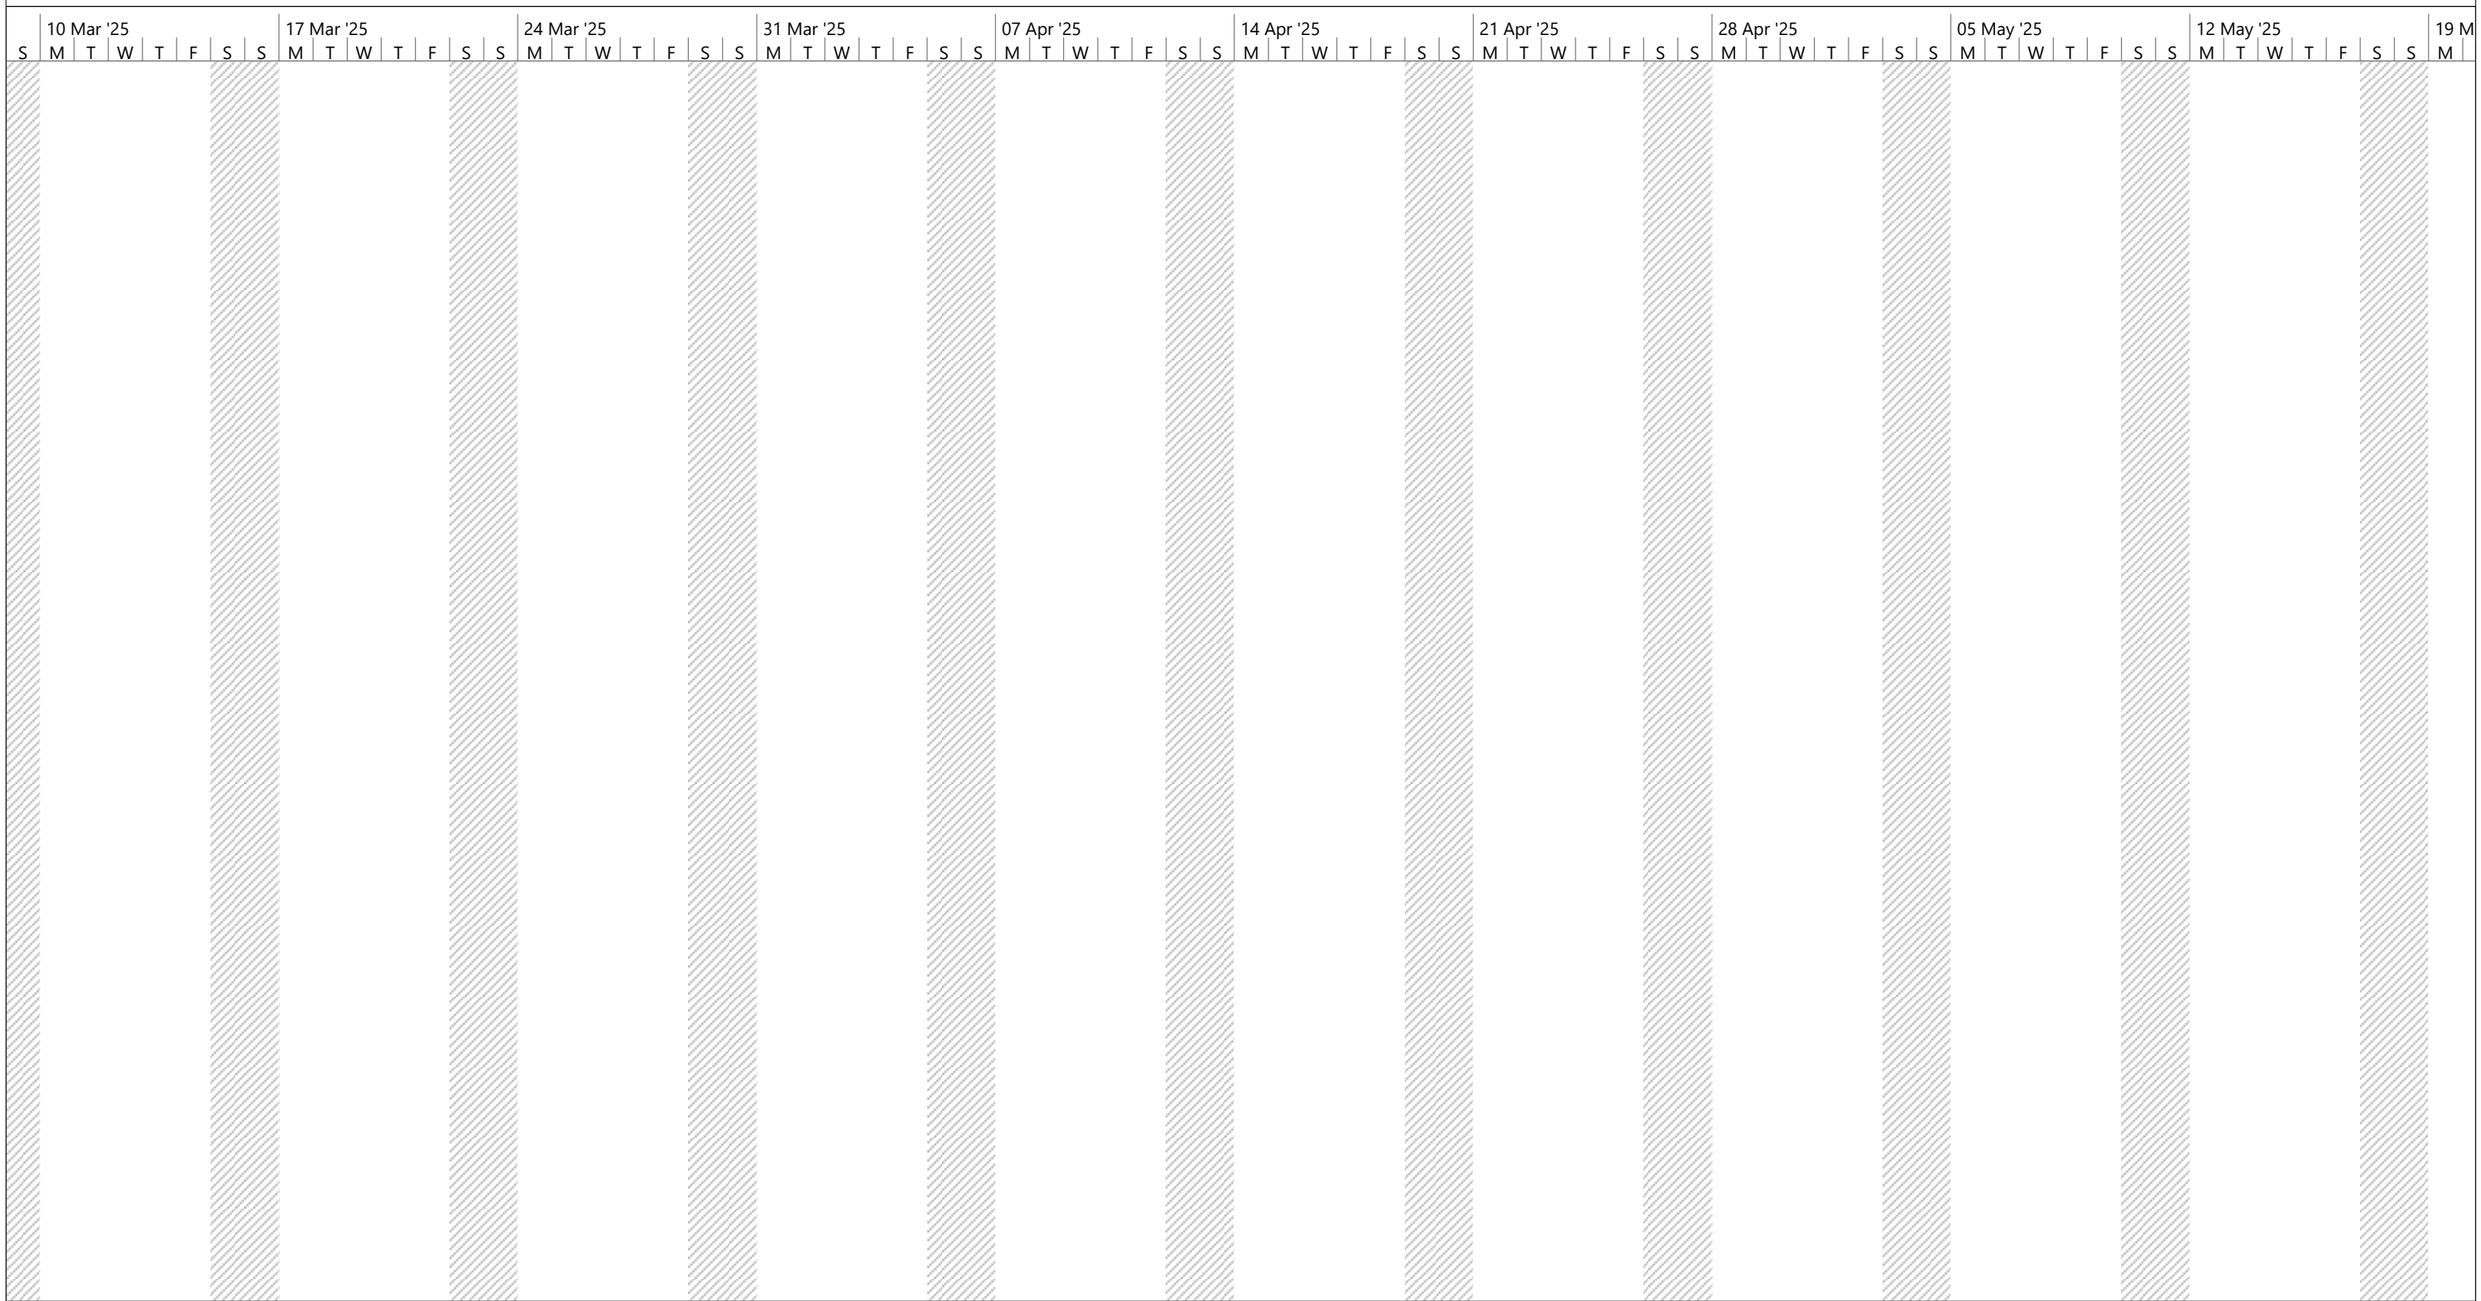

Programme

Greyline
Taking care of homes

May '25 | 26 May '25 | 02 Jun '25 | 09 Jun '25 | 16 Jun '25 | 23 Jun '25 | 30 Jun '25 | 07 Jul '25 | 14 Jul '25 | 21 Jul '25 | 28 Jul '25

T W T F S S | M T W T F S S | M T W T F S S | M T W T F S S | M T W T F S S | M T W T F S S | M T W T F S S | M T W T F S S | M T W T F S S | M T W T F S S | M T W

Programme

Greyline
Taking care of homes

| T | F | S | S | 04 Aug '25 M | T | W | T | F | S | S | 11 Aug '25 M | T | W | T | F | S | S | 18 Aug '25 M | T | W | T | F | S | S | 25 Aug '25 M | T | W | T | F | S | S | 01 Sep '25 M | T | W | T | F | S | S | 08 Sep '25 M | T | W | T | F | S | S | 15 Sep '25 M | T | W | T | F | S | S | 22 Sep '25 M | T | W | T | F | S | S | 29 Sep '25 M | T | W | T | F | S | S | 06 Oct '25 M | T | W | T | F |
|---|---|---

Programme

Greyline
Taking care of homes

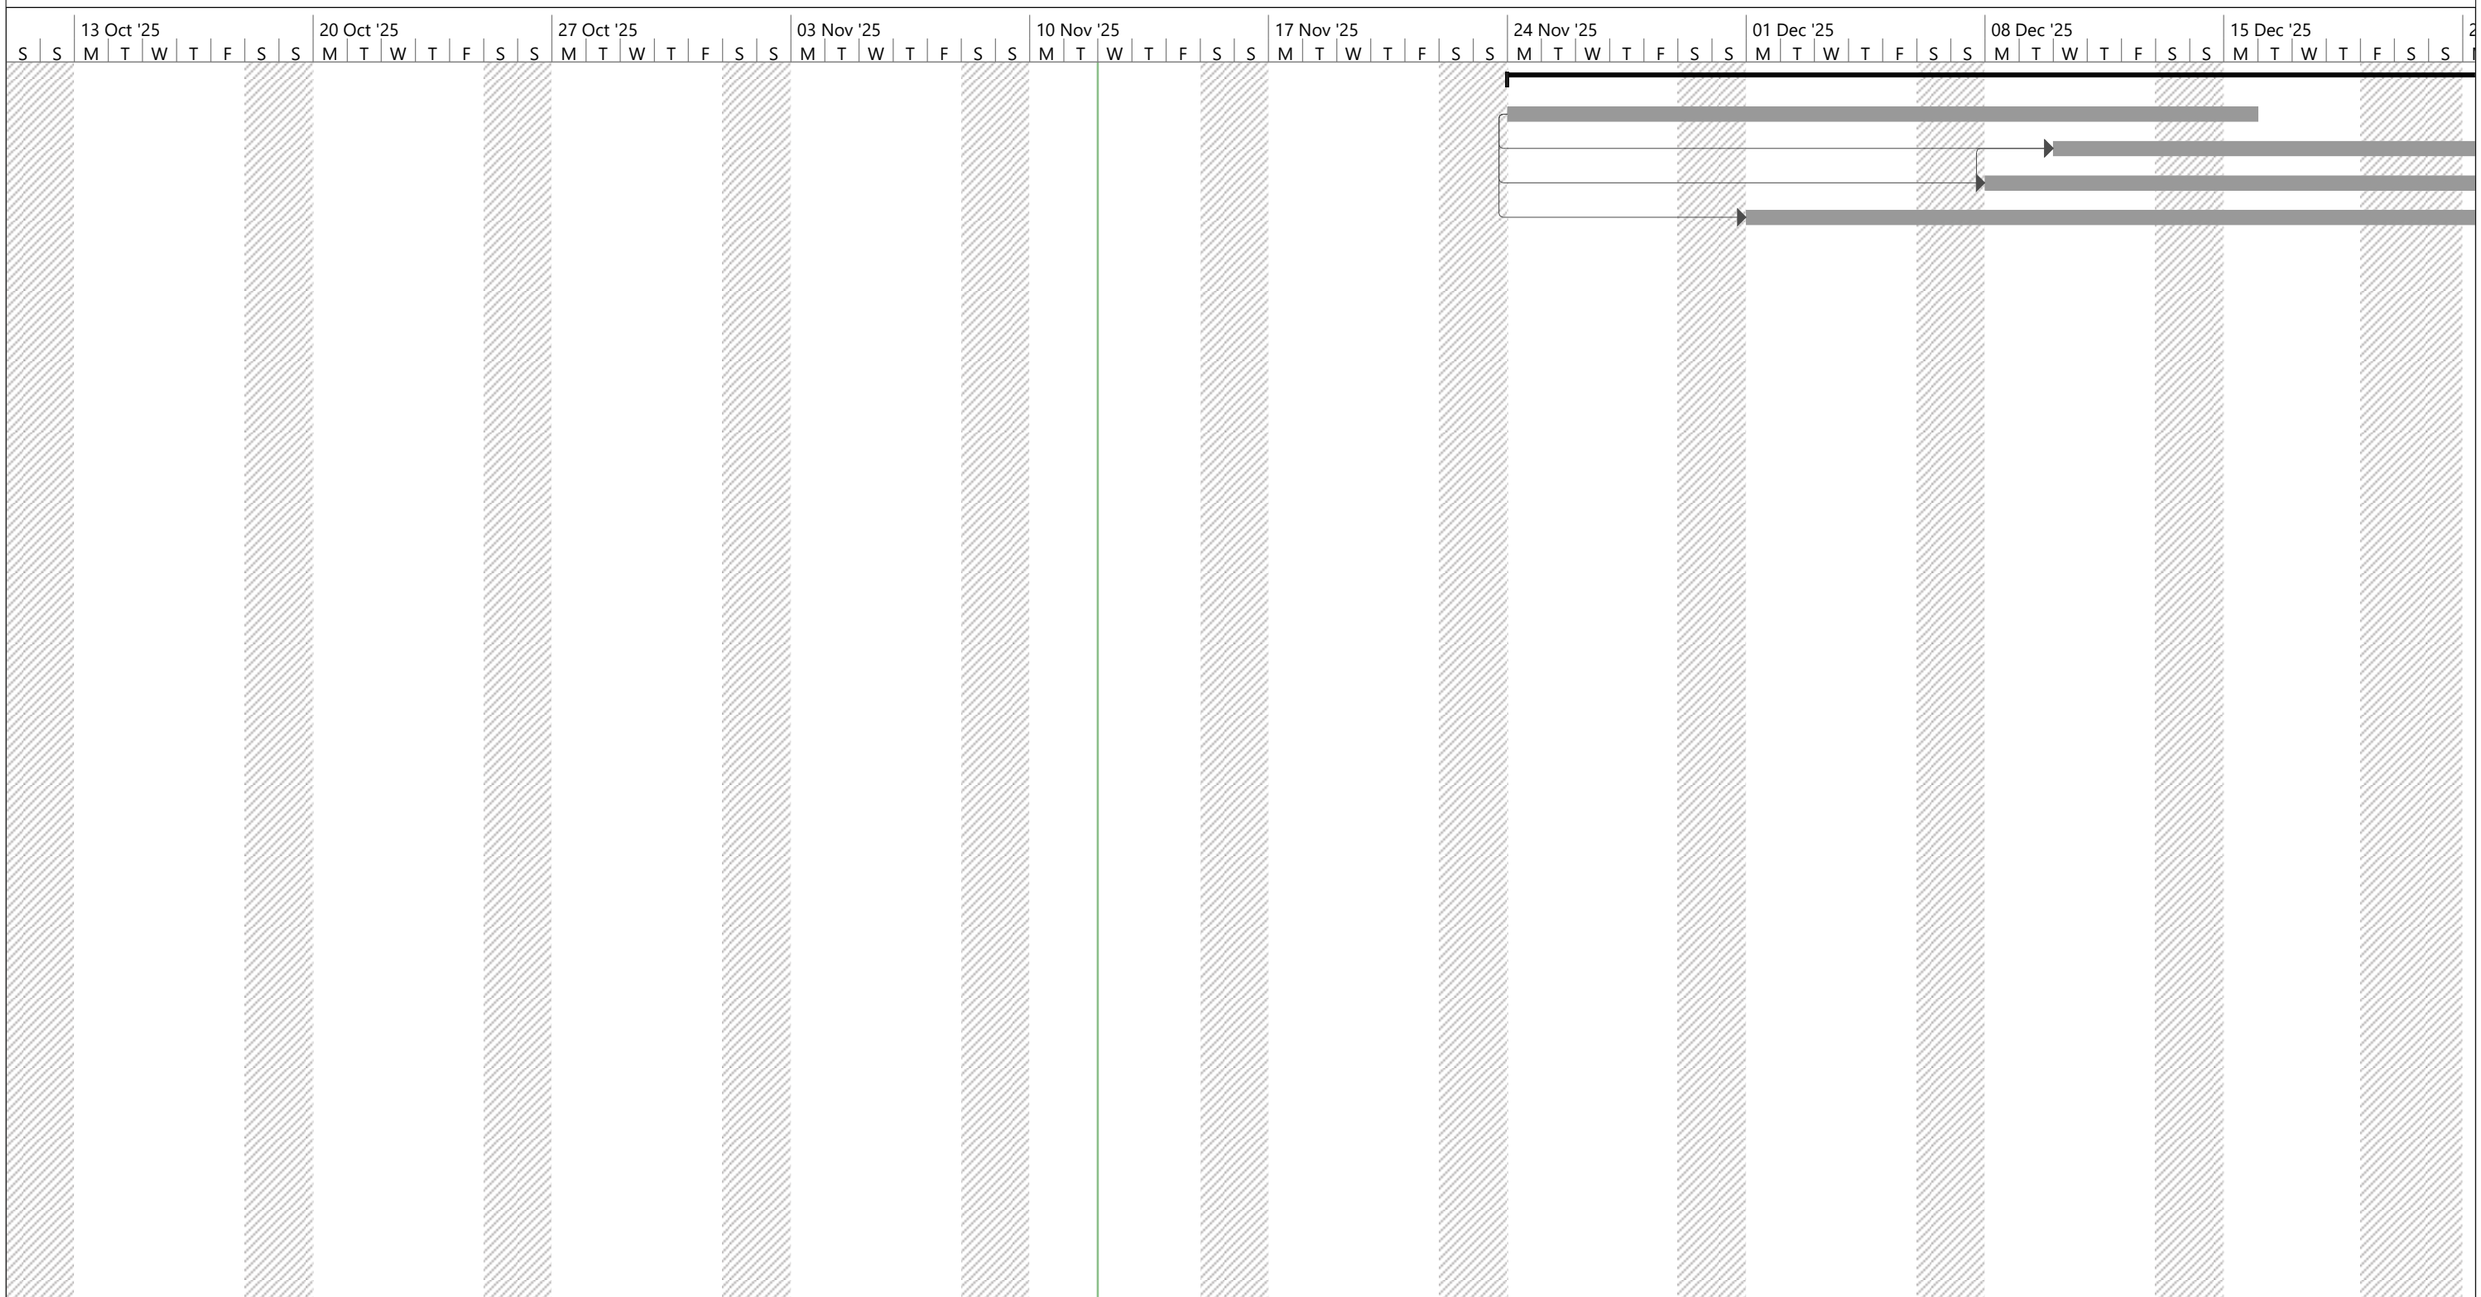

Programme
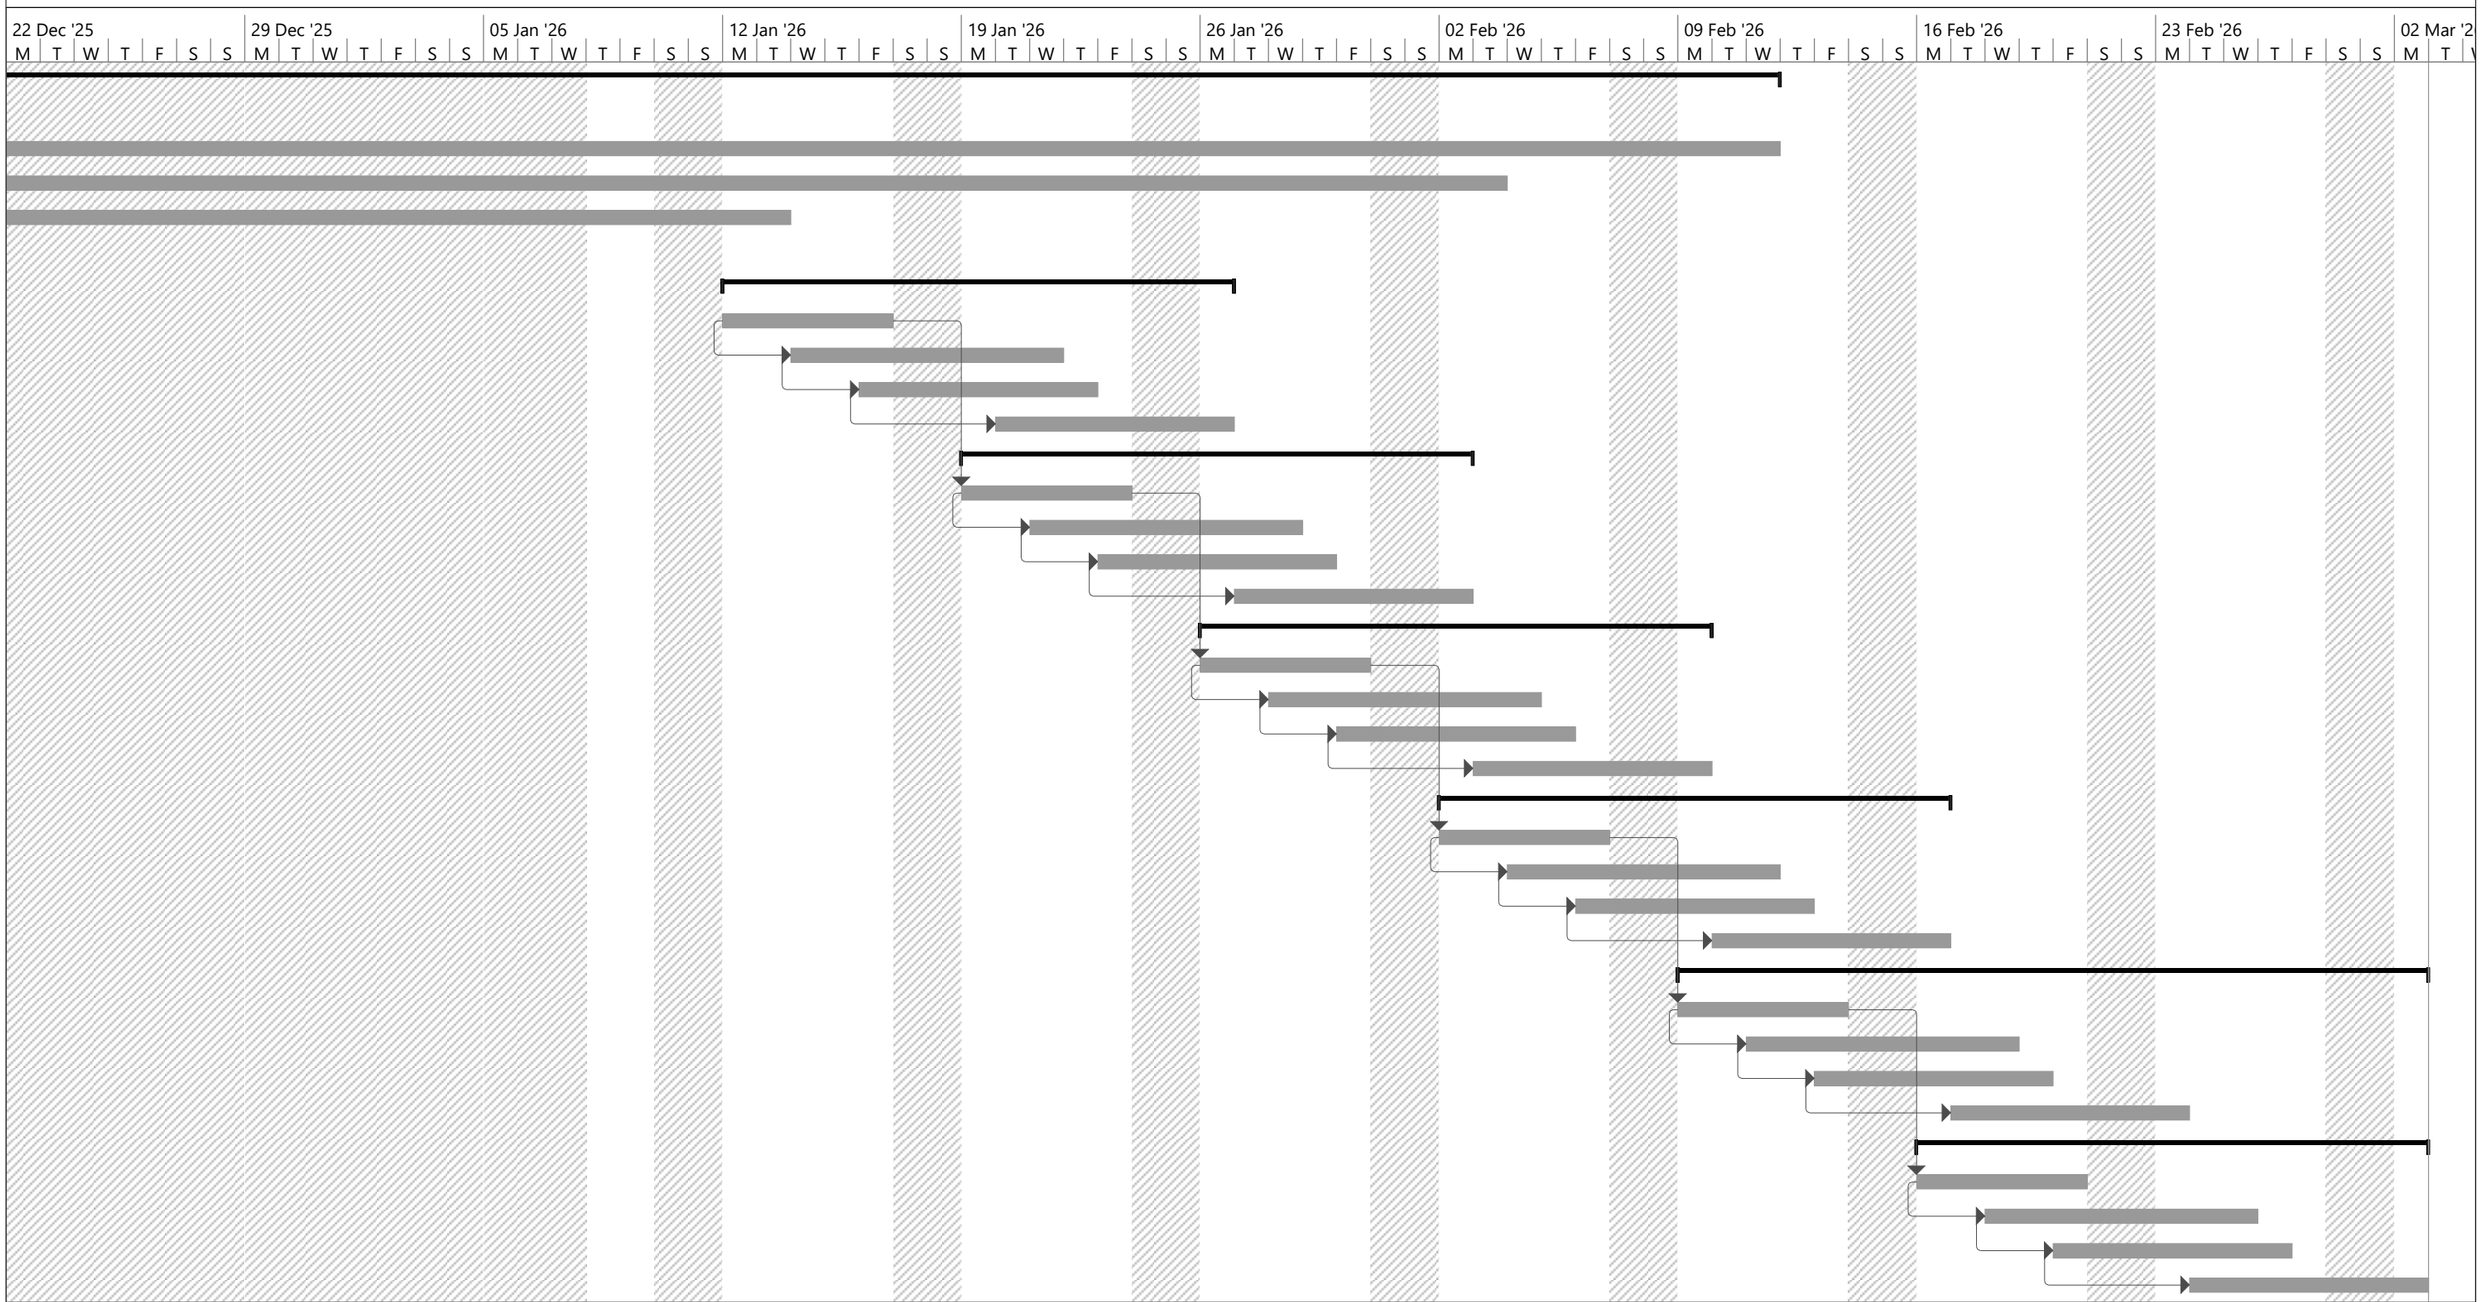
Greyline
Taking care of homes
